Where the Business Analyst Operates Determines the Return

Position upstream of investment decisions and ROI is exponential. Position downstream and it is capped.



UPSTREAM	DOWNSTREAM
HIGH-LEVERAGE BA	TRADITIONAL BA

SHAPES THE INVESTMENT

JOBS TO BE DONE

- Help leaders decide what **not** to fund
- Prevent low-value initiatives entering the pipeline
- Reduce cost before money is committed
- Redirect capital to higher-value opportunities
- Ensure benefits claimed are benefits realised
- Improve enterprise return on change investment

RETURN ON INVESTMENT

10–20×

$180K cost
$1.35M+ annual value
on a $10–30M portfolio

SUPPORTS THE DELIVERY

ACTIVITIES

- Elicit and document business requirements
- Support solution design and delivery teams
- Manage requirements change
- Engage stakeholders during delivery
- Assist with testing and implementation
- (Investment decisions already made)

RETURN ON INVESTMENT

1–3×

Same cost
Capped by post-decision scope
Optimisation, not multiplication

THE STRUCTURAL DIFFERENCE

The high-leverage BA **determines whether the work should exist at all**. The traditional BA **improves how the work is delivered**.

Both are valuable. Only one produces order-of-magnitude returns. The difference is not capability or effort. It is **positioning** — where in the lifecycle the BA enters the conversation.

BA Deliverables by Project Type

The two foundations apply to every initiative. Each tier inherits from the tier below.

FOUNDATIONS — APPLY TO ALL TIERS

Project Vision

Six elements. ~5–6 pages at full depth (lighter for Bronze).
Problem · Outcome · Scope · Stakeholders · Solution view · Measures.

As-Is and To-Be Analysis

Operational reality of how the business works today, connected to the design of how it will work tomorrow.

BRONZE

Simple Initiatives

Single team, single system, low risk

4 NEW · 4 TOTAL

FOUNDATION TIER

- **Project Brief**
  Need, success criteria, scope, sign-off
- **Requirements Summary**
  3–5 user stories with acceptance criteria
- **Configuration Guide**
  Setup specs, logic, permissions, test results
- **Handover Package**
  User guide, support contacts, 2-week review

EFFORT	TIMELINE
3–5 days	2 weeks

INHERITS →

SILVER

Standard Initiatives

Multiple stakeholders, meaningful change

8 NEW · 12 TOTAL

+ ALL BRONZE DELIVERABLES

- **Business Case**
- **Stakeholder Analysis**
- **Requirements Specification**
- **As-Is and To-Be Process Models**
- **Solution Design**
- **Data Contracts**
- **Test Plan and Results**
- **Training and Benefits Tracking**

EFFORT	TIMELINE
15–20 days	6–8 weeks

INHERITS →

GOLD

Strategic Initiatives

Enterprise-wide, executive sponsored

12 NEW · 24 TOTAL

+ BRONZE + SILVER

- **Strategic Business Case**
- **Enterprise Stakeholder Plan**
- **Enterprise As-Is Analysis**
- **Enterprise To-Be Design**
- **Enterprise Requirements**
- **Solution Architecture**
- **Data Strategy and Governance**
- **Implementation Roadmap**
- **Quality Assurance Framework**
- **Change Management Plan**
- **Operations Handbook**
- **Benefits and Risk Management**

EFFORT	TIMELINE
40–60 days	3–6 months

HOW TO READ THIS

Each tier card lists only the deliverables that are **new at that tier**. The inheritance badge declares what is carried forward. A Silver initiative therefore produces 12 deliverables in total (4 Bronze + 8 Silver). A Gold initiative produces 24 (4 Bronze + 8 Silver + 12 Gold). The foundations — Project Vision and As-Is/To-Be — are present in every tier and are not counted as deliverables.

BAS

BAS · VERSION 1.0

DELIVERY TIERS AT A GLANCE

Bronze, Silver, Gold — match the depth of analysis to the value at stake.

Every initiative passes the two foundations (Project Vision, As-Is/To-Be) before tier classification. Tiers are cumulative: Silver builds on Bronze; Gold builds on Silver.

CHOOSING THE TIER

Score the initiative on five factors — Cost · Risk · Reach · Reversibility · Strategic Visibility. Mostly small = Bronze. Mostly medium = Silver. Mostly large, or two reds = Gold.

BRONZE Simple Initiatives

4 artefacts

Configuration-class change in a single system. Well understood; consequences contained.

EXAMPLES

New report; new field; small workflow update; permission change.

DURATION · EFFORT

2–6 weeks (typical) · 0.25–0.5 FTE BA

RISK WINDOW

Low — reversible within current systems.

APPROVAL

Operational sign-off; no business case required.

KEY ARTEFACTS

Project Brief (what/why/who, 1 page) · Requirements Summary · Configuration Guide · Handover Package

SILVER Standard Initiatives

8 added (12 cumulative)

Multi-team change touching systems, processes, or data. Build, integration, meaningful business change.

EXAMPLES

New customer journey; cross-system integration; process redesign across two or more teams.

DURATION · EFFORT

3–9 months · 0.5–1 FTE BA across phases

RISK WINDOW

Moderate — recoverable with planned remediation.

APPROVAL

Funded business case; investment committee approval.

KEY ARTEFACTS

Business Case · Stakeholder Analysis · Requirements Spec · Process Models (As-Is + To-Be) · Solution Design + Data Contracts · Test Plan + Training & Benefits

GOLD Strategic Initiatives

12 added (24 cumulative)

Enterprise-scale transformation with board funding. Failure would be systemic or reputational.

EXAMPLES

Core platform replacement; multi-year transformation; cross-agency programme; regulatory build.

DURATION · EFFORT

12–36+ months · 2–5 FTE BAs + lead

RISK WINDOW

Strategic — failure damages operating model or balance sheet.

APPROVAL

Board-approved strategic business case; quarterly value reporting.

KEY ARTEFACTS

Strategic Business Case · Enterprise Stakeholder Plan · Enterprise As-Is + To-Be · Enterprise Requirements + Solution Architecture · Data Strategy + Roadmap + QA Framework · Change Mgmt + Ops Handbook + Benefits/Risk

BAS

BAS · VERSION 1.0

THE BACOE IMPLEMENTATION PATHWAY

Three phases over 24 months, each with defined artefacts and a decision gate.

Skipping phases is the most common cause of failure.

PHASE 1 — Readiness

MONTHS 0–3

PURPOSE

Confirm preconditions are present and the executive will support it.

KEY ACTIVITIES

- Diagnose current state and BA capability
- Identify executive sponsor and reporting line
- Define operating boundaries with PMO, CIO/CTO, transformation office
- Build executive business case
- Secure three-year funding commitment

ARTEFACTS PRODUCED

Current State Diagnostic · BA Capability Heat-Map · Operating Boundaries Agreement · Executive Business Case · Funding Decision

GATE: Three-year funding secured?

PHASE 2 — Pilot

MONTHS 3–9

PURPOSE

Demonstrate value mechanisms on a contained set of initiatives.

KEY ACTIVITIES

- Recruit BACOE Lead and 2–3 senior BAs
- Define core artefacts and standards
- Place senior BAs on 3–5 high-leverage initiatives
- Establish governance forum
- Track value contribution from day one

ARTEFACTS PRODUCED

Core BACOE Templates and Standards · Service Catalogue · Governance Terms of Reference · First Quarterly Value Report

GATE: Quantified value on 3+ initiatives?

PHASE 3 — Scale and Embed

MONTHS 9–24

PURPOSE

Extend reach across the portfolio and embed the practice for the long run.

KEY ACTIVITIES

- Extend coverage to full priority portfolio
- Recruit to target structure
- Launch BA Community of Practice
- Establish capability framework and pathways
- Move benefits-tracking to portfolio level
- Establish annual board review

ARTEFACTS PRODUCED

BACOE Operations Handbook · BA Capability Framework · Portfolio-Level Benefits Report · Annual Board Report · Year 2 and Year 3 Value Reports

EMBEDDED: Portfolio-level reporting active?

Readiness is the only phase where stopping is the correct outcome. If preconditions are not met, do not proceed — a half-funded BACOE in a hostile environment is worse than no BACOE.

Compressing below twelve months usually skips Readiness or Pilot and pays the cost in Year 2 with a defunding

BAS

BAS · VERSION 1.0

THE BA ROLE FAMILY — EXTENDED

Adapted from Clare (2008) and the IIBA Career Road Map. Teal highlights are the four BAS practice roles.

Adapted from Clare (ed.) 2008, p.168 and the IIBA Business Analyst Career Road Map. Modern adjacent families and the Architecture family added for 2026 practice context.

ADJACENT JOB FAMILIES — TRADITIONAL AND MODERN

- Business Operations
- QA / Tester
- Application Development
- Product Management
- Agile / Delivery
- Data & Analytics
- UX / Service Design

BA JOB FAMILY — THE CAREER SPINE

- Entry Level BA
- Associate BA
- Business Analyst (4)
- Senior Business Analyst (3)
- Lead Business Analyst (2)

Specialty BA Roles
Process · Rules · Agile · Data · Technical

Entry Level / Associate develop into BA with experience. Lead BA feeds the BA Practice Lead role below.

BA LEADERSHIP JOB FAMILY

- BA Project Lead
- BA Program Lead
- Strategic BA
- Relationship Manager
- BA Manager
- BA Practice Lead (COE Leader) (1)

PROJECT, PROGRAMME & PRODUCT

Project Management
Project Manager · Senior PM · Program Manager · PMO Leader

Product Management
Product Owner · Product Manager · Senior PM (Product) · Head of Product

Agile / Delivery
Scrum Master · Agile Coach · Release Train Eng. (SAFe) · Delivery Manager

Data, Analytics & UX
Data Analyst · Data Scientist · UX Researcher · Service Designer

ARCHITECTURE JOB FAMILY

- Enterprise Architect
- Business Architect
- Solution Architect
- Data Architect
- Process Architect
- Application / Technical Architect
- Integration Architect
- Security Architect
- Cloud Architect
- Information Architect
- AI / ML Architect
- Domain Architect

ORGANISATIONAL SENIOR LEADERSHIP

- Business Unit Management
- Strategic Capabilities Delivery Leader
- IT Management
- Senior Leadership / C-Suite

BAS

BAS · VERSION 1.0

WHAT A BACOE COSTS

Indicative staffing and cost ranges by enterprise size. AUD, 2026 Australian market.

Cost scales with portfolio size, organisational complexity, and the maturity of the existing BA community. The four roles below are the same as those defined in the Roles section. Ratios travel; absolute dollars do not.

SMALL — Change portfolio $5M – $30M

ROLE	FTE	ANNUAL
BA Practice Lead	1.0	**$250k**
Lead Business Analyst	1.0	**$220k**
Senior Business Analyst	2.0	**$400k**
Business Analyst	1.0	**$140k**
Tooling and platforms	—	**$40k – $80k**
Setup costs (Year 1)	—	**$100k – $200k**

Steady-state annual	**$1.0M – $1.2M**	Year 1 annual	**$1.1M – $1.4M**
Total FTE	**5.0**	% of portfolio	**~3%**

MID-SIZE — Change portfolio $30M – $100M

ROLE	FTE	ANNUAL
BA Practice Lead	1.0	**$250k**
Lead Business Analyst	2.0	**$440k**
Senior Business Analyst	3.0 – 4.0	**$600k – $800k**
Business Analyst	2.0 – 3.0	**$280k – $420k**
Tooling and platforms	—	**$80k – $150k**
Setup costs (Year 1)	—	**$200k – $400k**

Steady-state annual	**$1.7M – $2.2M**	Year 1 annual	**$1.9M – $2.6M**
Total FTE	**8.0 – 10.0**	% of portfolio	**~2 – 3%**

LARGE — Change portfolio $100M+

ROLE	FTE	ANNUAL
BA Practice Lead	1.0	**$300k**
Lead Business Analyst	3.0 – 4.0	**$660k – $880k**
Senior Business Analyst	6.0 – 9.0	**$1.2M – $1.8M**
Business Analyst	3.0 – 5.0	**$420k – $700k**
Tooling and platforms	—	**$150k – $300k**
Setup costs (Year 1)	—	**$400k – $800k**

Steady-state annual	**$3.0M – $4.0M**	Year 1 annual	**$3.4M – $4.8M**
Total FTE	**13.0 – 19.0**	% of portfolio	**~3 – 4%**

A NOTE ON GEOGRAPHY — Multiply senior BA loaded cost by ~0.55 for UK (GBP), ~1.05 for US East/West coasts, ~0.75 for US mid-market. Focus on ratios: BACOE cost as % of portfolio (1–3% small, 2–3% mid, 3–4% large) and proportional allocation across roles, tooling, and setup. The ratios travel; the dollar figures do not.

1 DEMAND & CONTEXT

ELEMENT 1

Problem

What is wrong today, in business language. What is happening? Where is the friction? Who is affected? Where do delays appear?

Test: stakeholders should recognise their own world. Two to four paragraphs.

ELEMENT 2

Desired Outcome

What success looks like. What will be different operationally? What improvement is expected? How will it be measured?

Convert every aspiration to a measurable target. "Faster" becomes "under 10 minutes."

2 PROBLEM FRAMING

ELEMENT 3

Scope Boundaries

In Scope
Named channels, segments, systems

Out of Scope
Explicit exclusions stakeholders may have assumed

Constraints
Fixed elements (deadlines, budget, platform decisions)

Assumptions
Stated explicitly so they can be tested

ELEMENT 4

Stakeholders

Decision Makers
Authority to fund, scope, or stop

Business Owners
Own the operational outcome

Key Users
Use the new capability daily

Delivery Enablers
Technical, compliance, supporting teams

Named, not generic.

3 SOLUTION DIRECTION

ELEMENT 5

Early View of the Solution

Direction of travel. Not a design. A plausible shape that aligns thinking without committing to implementation.

Acceptable forms:

- Rough process flow
- Workflow diagram
- High-level system view
- Dashboard or screen concept

A paragraph of prose plus a single diagram or sketch.

[Diagram or sketch here]

Test: stakeholders say "yes, that's the kind of thing we mean."

If "no, we were thinking of something different" — return to Element 1.

4 MEASURES OF SUCCESS

ELEMENT 6

Measures of Success

How the initiative will be judged. Five to seven measures. Mix of leading and lagging.

Per measure:

- Metric — what is measured
- Baseline — current value
- Target — post-delivery value
- Timing — when measured
- Owner — accountable role
- Type — leading or lagging

Leading measures
Early indicators (e.g. adoption at 30 days)

Lagging measures
Delayed indicators (e.g. cost per unit at 12 months)

Without explicit measures, initiatives declare success without evidence.

5 SIGN-OFF

COVER PANEL

Initiative Name

_____

Sponsor

_____

Business Owner

_____

APPROVAL

This Project Vision is approved as the basis for delivery.

Sponsor
Name: _____
Date: _____
Signature: _____

Business Owner
Name: _____
Date: _____
Signature: _____

VERSION CONTROL

Version: _____
Next Review:
at end of As-Is/To-Be analysis

1 DEMAND & CONTEXT

PROBLEM

New retail account onboarding takes 4–7 business days. Paper forms, manual data entry, batch overnight KYC review.

Customer drop-off at three points: 22% after paper forms (no acknowledgement); 18% during verification (document burden); ~5% at funding (account invisible in app).

Branch staff: 35–40% of customer time on data entry, not advice.

DESIRED OUTCOME

Eligible accounts complete in **under 10 minutes** on web or mobile. Secure eKYC, automated identity verification, real-time decisioning.

Total drop-off: 40% → **under 8%.**
Branch data-entry: 35% → **under 10%.**
Compliance backlog eliminated; 95% of reviews within 30 minutes.

Compliance posture preserved.

2 PROBLEM FRAMING

SCOPE BOUNDARIES

In Scope
Digital onboarding · Individuals + SME · web + mobile · core banking, KYC vendor, CRM · KYC/AML and PCI-DSS compliance

Out of Scope
Wealth management onboarding · loan origination · post-onboarding servicing · international branches · core platform replacement

Constraints
AML rules deadline end FY26 · $1.5M budget envelope · existing core banking platform retained

Assumptions
KYC vendor APIs stable · ID verification SLAs hold · CRM absorbs new data model

STAKEHOLDERS

Decision Makers
Jane Smith — Head of Retail Banking
Sarah Lee — Head of Risk & Compliance

Business Owners
Mark Johnson — Customer Operations
Priya Patel — Head of Finance

Key Users
Branch staff · Relationship managers · Customers (prospect)

Delivery Enablers
CIO · KYC vendor · Identity provider · Compliance team · Core banking team

Engagement schedule attached.

3 SOLUTION DIRECTION

EARLY VIEW OF THE SOLUTION

Digital-first onboarding journey starting in customer's chosen channel. Captures identity through eKYC and document verification. Real-time risk and AML scoring via existing KYC vendor. Branch and contact-centre journeys retained as fallback.

Five-step flow:



Each step automated. Manual review triggered only on exception.

Integrations:

eKYC vendor | Core banking | CRM

Direction confirmed by Mark Johnson and Sarah Lee in workshop, 18 May 2026.

Options under consideration:

- Build in-house
- Buy COTS solution
- **Partner / SaaS (preferred)**
  Best balance of speed, value, risk — see Options Analysis.
- Do nothing (rejected)

4 MEASURES OF SUCCESS

SIX MEASURES

1. Time to account activation
4–7 days → under 10 min for 80%
3 months · Head of Retail · Leading

2. Application drop-off rate
40% → under 8%
3 months · Customer Ops · Leading

3. Branch data-entry time share
35% → under 10%
6 months · Head of Retail · Leading

4. Cost per account opened
$84 → under $58 (–30%)
12 months · Head of Finance · Lagging

5. Net new accounts per month
Today's run-rate · +40% target
12 months · Head of Retail · Lagging

6. Compliance review SLA
200–300 backlog → 95% within 30 min
3 months · Head of Risk · Leading

Estimated annual value
$2.4M cost savings + revenue
Investment: $1.2–1.5M build · 12 mth ROI payback · 18–24 mth full benefit

Tracking
Monthly review by Customer Operations Director from Month 1.

Quarterly executive review with Sponsor through Year 2.

Year 1 Benefits Realisation Plan attached as supporting document.

5 SIGN-OFF

COVER

Initiative
Digital Onboarding Transformation

Reference
FIN-2026-017

Tier GOLD (strategic)

Date
20 May 2026

APPROVAL

Approved as the basis for delivery.

Sponsor
Jane Smith
Head of Retail Banking
20 May 2026 *[J. Smith]*

Business Owner
Mark Johnson
Customer Operations Director
20 May 2026 *[M. Johnson]*

Co-signed (Compliance)
Sarah Lee
Head of Risk & Compliance

VERSION

v1.0 · 20 May 2026
Next review: end of As-Is/To-Be analysis · target ~15 June 2026

AS-IS — OPERATIONAL REALITY TODAY

SECTION 1

Current Process Flow

End-to-end flow from trigger event to outcome. Each major step in sequence.
Roles, systems, handoffs, decision branches all explicit.

Built by walking the work with the people who do it. Not by reading process documentation.

Documentation describes the official process; the As-Is must describe the actual one.

Format: Single diagram + 1–2 page narrative + named operators who validated

SECTION 2

Pain Points & Workarounds

For each step:

- **Delays** — where does work wait?
- **Errors** — where do mistakes happen?
- **Data breakdowns** — what fails to flow?
- **Workarounds** — what informal practices?

Workarounds reveal where the official process is failing.

SECTION 3

Systems & Data Flow Map

For each system:

- What it does, who owns it
- Data passed in / out, format, cadence
- Manual rekeying or transformations
- Known issues per flow

Most process pain has a data dimension.

QUANTIFICATION

Quantify pain points where data permits

"Slow" is weak. "Average 3-day wait, 30% of cases" is actionable.
Tie each pain point to a specific step in the flow.
Connect pain points back to the Problem Statement in the Project Vision.

Output: Pain Points Inventory with step, type, description, quantification, why it exists

Confirmed by named operators who do the work.

TO-BE — DESIGN OF HOW IT WILL WORK

SECTION 4

To-Be Process & System Design

Future process flow + system flow. Two layers, must be consistent.

Must:

- Address every pain point from Section 2 — resolved or accepted
- Eliminate or formalise every workaround
- Map cleanly to Desired Outcome in Project Vision

Test: stakeholder sees As-Is and To-Be side by side and clearly sees the improvement.

SECTION 5

Pain Point Resolution

For each pain from Section 2:

- **Fully resolved** — gone in To-Be
- **Partially mitigated** — reduced
- **Accepted** — known limitation

Honesty matters. Don't claim resolution that won't materialise.

SECTION 6

Capability & Role Changes

Per role:

- **New** — did not exist before
- **Changed** — work content shifts
- **Reduced** — volume decreases
- **Eliminated** — no longer needed

Surface contentious findings here, not after delivery.

SIGN-OFF

Approved as the basis for solution design and delivery

Sponsor Name · Title · Date · Signature


Business Owner Name · Title · Date · Signature

Project Vision referenced: Version __, dated __

A To-Be that does not connect to a verified As-Is is a future state designed in a vacuum.
Without sign-off here, delivery design proceeds at risk.

AS-IS — TODAY (BASELINE FY26 Q1)

CURRENT PROCESS FLOW



Confirmed by 2 Tier 1 officers, 1 Tier 2 officer, the Medical Reviewer team lead, March 2026.

PAIN POINTS

P1. Tier 2 precedent lookup
No system view of past decisions; officers maintain personal spreadsheets.
~30 min/case · 200+ cases/officer/month

P2. Information requests
35% of Tier 2 cases re-loop to patients; average 9-day delay added.

P3. Mailroom indexing accuracy
Manual indexing — 4% mis-routed

SYSTEMS & DATA

Claims Platform (legacy 1998)
No precedent lookup · no API for analytics

Document Management
Indexed manually · OCR confidence not used

Member Portal
Status update only after Tier 1 decision — 3-day visibility gap drives 12% support calls

Most pain has a data dimension.


QUANTIFIED BASELINE

Mean claim cycle:	**8.5 days**	(SLA: 5 days · met on 41% of claims)
Tier 2 escalation rate:	**43%**	(industry benchmark: 25–30%)
Member satisfaction:	**62%**	(industry benchmark: 78%)
Annual cost of process:	**$8.4M**	(staff $6.1M, systems $1.4M, error rework $0.9M)

Pain points P1–P3 are tied to Problem Statement in Project Vision HC-2026-042.

TO-BE — TARGET (FY27 Q4)

TO-BE PROCESS & SYSTEM DESIGN



Validated against Project Vision Desired Outcome — meets all six measures.

PAIN POINT RESOLUTION

P1. Precedent lookup — RESOLVED
AI-augmented precedent surfaced inline

P2. Information requests — RESOLVED
Required documents requested upfront

P3. Mailroom indexing — PARTIALLY
Digital-first; paper path retained for 5% of members; OCR confidence flag added

All 3 pain points addressed.

ROLE CHANGES

Tier 1 Claims Officer — REDUCED
~40% headcount reduction over 18 months via natural attrition; remaining work shifts toward exception handling.

Triage Operations Analyst — NEW
2 FTE — monitor AI accuracy, tune rules

Tier 2 / Medical Review — CHANGED
Higher proportion of complex cases

SIGN-OFF

Approved as the basis for solution design and delivery

Sponsor	David Chen — Chief Operating Officer · 12 June 2026 ·	*[D. Chen]*
Business Owner	Lisa Park — Head of Claims Operations · 12 June 2026 ·	*[L. Park]*
Co-signed	Dr Rachel Kim (Medical Director) · Tom Patel (CIO)	
Project Vision referenced:	HC-2026-042 v1.1 (revised post As-Is review, dated 5 June 2026)	

A To-Be that does not connect to a verified As-Is is a future state designed in a vacuum.

WHY THIS INITIATIVE EXISTS

SECTION 1

Business Need

A one-paragraph statement of the problem.
Drawn from the Project Vision Problem Statement, but condensed.

What is happening today that should not be?
Where is the friction? Who is affected?

Length: 3–5 sentences. Plain prose. No solution language.

SECTION 2

Success Criteria

Three to five specific, measurable outcomes.

- Each criterion has a number, percentage, or specific outcome
- Drawn from the Desired Outcome in the Project Vision
- Achievable in the timeline; not heroic
- Testable at the post-launch review

SECTION 3

Standard Performance Indicators

The 2–3 metrics that will be tracked post-delivery.

Per indicator: Metric · Baseline · Target · Cadence

Confirmed by the BAU team that will operate the result.

SCOPE AND APPROVAL

SECTION 4

Scope Boundaries

In Scope
Specific deliverables and capabilities the initiative will produce. Single-line bullets.

Out of Scope
Explicit exclusions. Even Bronze-tier initiatives need explicit out-of-scope items — they prevent the most common Bronze failure: scope drift.

Assumptions
What must be true for delivery to succeed.

SECTION 5

Stakeholder Agreement and Sign-off

Three named people. Signed before delivery starts.

Business Owner	Name: _____	Date: _____
Implementer	Name: _____	Date: _____
Analyst	Name: _____	Date: _____

"Yes, that is what I want." — the Project Brief is the artefact that the business owner signs to confirm this.

AGREED DELIVERY DATE

Target date: _____
Two-week post-launch review scheduled at: _____

WHY THIS INITIATIVE EXISTS

BUSINESS NEED

Store managers do not have a daily view of sales, stock, and footfall consolidated in one place. They currently pull data from three reports (point-of-sale, ERP, sensor system) plus a manual spreadsheet, taking **30–45 minutes each morning before the store opens.**

This delays merchandising decisions and creates inconsistency between stores. Regional managers cannot get a comparable view across their stores until the next-day batch report runs at 11am.

SUCCESS CRITERIA

1. Single dashboard available by 7am daily
Showing sales-vs-budget, stock health, footfall — current day plus rolling 7-day trend.

2. Store manager preparation time reduces from 30–45 min to under 5
Measured via self-reported time at the two-week post-launch review.

3. Adopted by 90% of store managers within 4 weeks of launch
Adoption = at least one dashboard view per business day.

4. Regional managers can compare stores within a region in one view
Adds a regional-level filter and sort.

PERFORMANCE INDICATORS

PI-1. Daily active users (store managers)
Baseline: 0 · Target: 169 of 187 (90%) · Cadence: weekly automated count from BI

PI-2. Time-to-prep (self-reported)
Baseline: 30–45 min · Target: under 5 min · Cadence: post-launch survey at week 2

PI-3. Cross-store decision speed (regional)
Baseline: same-day decisions on 30% of issues · Target: 70% · Cadence: month 3

SCOPE AND APPROVAL

SCOPE BOUNDARIES

In Scope

- 187 stores in Australia (East and West regions)
- Power BI dashboard published to existing tenant; mobile + desktop access
- Daily refresh from POS (5:30am), ERP (direct query), footfall sensors

Out of Scope

- Stores without footfall sensors (4 stores) — sensor rollout is separate
- Intra-day refresh — deferred to FY27 if value warrants it
- Predictive analytics or forecasting — out of scope for this initiative

Assumptions

POS access granted · ERP read access pending IT approval (low risk)

STAKEHOLDER AGREEMENT

Approved as the basis for delivery.

Business Owner	Karen Liu — Regional Manager East	3 March 2026	*[K. Liu]*
Implementer	Sarah Lee — BI Operations Lead	3 March 2026	*[S. Lee]*
Analyst	Mark Johnson — Retail Operations BA	3 March 2026	*[M. Johnson]*

Three signatures gathered in 25-minute working session, 3 March 2026.
Implementer confirmed buildability before signing.

AGREED DELIVERY

Target launch: 12 March 2026 (9 working days from sign-off)
Two-week post-launch review: 28 March 2026 — pilot stores + Regional Manager East + Implementer + Analyst

WHAT NEEDS TO BE BUILT

SECTION 1 — USER STORIES (3–5)

Format: "As a [role], I want [capability], so that [outcome]"

Story 1

As a _____, I want _____
_____, so that _____

Story 2

As a _____, I want _____
_____, so that _____

Story 3

As a _____, I want _____
_____, so that _____

If you have more than 5 user stories — stop. The initiative is not Bronze.
Re-run the Tier Classifier.

SECTION 2 — ACCEPTANCE CRITERIA

For each user story, two to four specific tests that confirm the story is met.

Story 1 acceptance:

1.1 _____
1.2 _____
1.3 _____

Story 2 acceptance:

2.1 _____
2.2 _____

Acceptance criteria are testable, not subjective.
Each criterion is a specific behaviour that can be observed or measured.

DATA AND DEPENDENCIES

SECTION 3 — DATA SOURCES & ACCESS

Which systems, which feeds, which permissions.

SYSTEM	DATA NEEDED	ACCESS STATUS
_____	_____	_____
_____	_____	_____
_____	_____	_____

Status options: Granted · Pending request · Pending approval · Blocker

Pending or blocked access must be flagged before delivery starts.
Bronze initiatives stall most often on pending access, not technical issues.

SECTION 4 — DEPENDENCIES & ASSUMPTIONS

Dependencies

What must be in place for the work to succeed.

_____
_____

Assumptions

Tested or believed-to-be-true conditions.

_____
_____

IMPLEMENTER CONFIRMATION

"I have reviewed these requirements and confirm they are buildable as stated."

Implementer: _____ Date: _____

WHAT NEEDS TO BE BUILT

USER STORIES (3 STORIES)

Story 1 — Reorder stops in active route

As a **delivery driver**,
I want to **reorder upcoming stops in the mobile dispatch app**,
so that I can adapt to traffic, weather, or customer access changes without calling dispatch.

Story 2 — Dispatch sees the change

As a **dispatch coordinator**,
I want to **see driver-initiated stop reorders reflected in the dispatch console within 30 seconds**,
so that I can update customer ETAs and respond to escalations with current information.

Story 3 — Audit trail of changes

As an **operations manager**,
I want **a record of who reordered which stops and why**,
so that I can review patterns weekly and identify systemic routing issues.

ACCEPTANCE CRITERIA

Story 1:

1.1 Driver can drag-and-drop stops in their route list to reorder them
1.2 Reorder is permitted only for upcoming stops, not for completed or in-progress stops
1.3 Driver must select a reason from a dropdown (Traffic, Weather, Customer access, Other)
1.4 New ETA is recalculated and displayed within 5 seconds of confirming the reorder

Story 2:

2.1 Dispatch console shows updated stop order within 30 seconds of driver confirmation
2.2 Visual indicator on the route card flags driver-initiated changes (vs dispatch-initiated)

Story 3:

3.1 All reorder events stored in audit log: timestamp, driver, route, reason, original/new order
3.2 Operations manager can export the log for a date range as CSV

DATA AND DEPENDENCIES

DATA SOURCES & ACCESS

SYSTEM	DATA NEEDED	ACCESS STATUS
Dispatch Platform	Route data, stop sequence	**Granted**
Mobile Dispatch App	Driver UI, location feed	**Granted**
Customer Notification Service	ETA push API	**Pending**
Audit Log Database	Write access for new schema	**Granted**

Pending: Customer Notification Service team to confirm ETA push capacity by 10 March.

Customer Notification Service is non-blocking — Story 2 can deliver without it, customer ETA updates handled in next-sprint follow-up.

DEPENDENCIES & ASSUMPTIONS

Dependencies

- Mobile app v3.4 must be released to drivers (rolling deployment, March 1–8)
- Audit Log Database schema migration approved by DBA team (request raised)

Assumptions

- Driver mobile devices have stable connectivity to confirm reorders (validated)
- Existing dispatch console refresh cadence supports 30-second update target

IMPLEMENTER CONFIRMATION

"I have reviewed these requirements and confirm they are buildable as stated."

Implementer: Daniel Ng — Senior Mobile Developer 5 March 2026 *[D. Ng]*

HOW IT WAS BUILT

SECTION 1 — SETUP SPECIFICATIONS

The technical configuration applied. System settings, parameters, integrations.

Platform / Tool

_____

Workspace / Tenant

_____

Connections / Integrations

_____

_____

Refresh / Schedule

_____

Detail enough that another implementer could reproduce the configuration.

SECTION 2 — FILTERS & LOGIC

The business rules implemented. Data filters, calculation logic, display logic.

Calculations

_____

_____

Filters

_____

_____

Display Rules

_____

_____

Business rules in plain language. Code snippets where they help.

PERMISSIONS AND TEST RESULTS

SECTION 3 — USER PERMISSIONS

Who has access, at what level, through what mechanism.

ROLE / GROUP	ACCESS LEVEL	MECHANISM
_____	_____	_____
_____	_____	_____
_____	_____	_____

Mechanism options: Active Directory group · Application role · Direct grant · Inherited

Permissions must be by group, not by individual, wherever possible — for portability.

SECTION 4 — TEST RESULTS

Confirms the build meets the acceptance criteria from the Requirements Summary.

CRITERION	RESULT	TESTED ON
_____	Pass / Fail	_____
_____	Pass / Fail	_____
_____	Pass / Fail	_____

All criteria from the Requirements Summary should appear here. None should be skipped.

CONFIGURATION SIGN-OFF

Implementer: _____ Date: _____

"This guide accurately describes the configuration deployed."

HOW IT WAS BUILT

SETUP SPECIFICATIONS

Platform Tableau Server (existing university tenant)

Workspace Project: `Academic Operations` · Workbook: `Faculty Enrolment Health v1.0`

Connections

- Student Information System (PeopleSoft) — Live connection via SSO; read-only role `RPT_VIEW`
- Course Catalogue (SQL Server) — Direct query, refresh every 60 minutes
- Finance System extract (CSV, daily) — staged in Azure Data Lake, ingested at 06:00 daily

Refresh Schedule Daily at 06:00 AEST · Manual refresh available for admins

Hosting Tableau Server, Site: `Academic` · URL: `/tab/faculty-enrolment`

Existing university tenant means no new platform cost. Refresh aligns with finance close.

FILTERS & LOGIC

Calculations

Enrolment-vs-target % = (current enrolments ÷ faculty target) − 1, displayed as %

Trend = enrolment count, last 4 weeks, displayed as sparkline

Withdrawal rate = withdrawals in last 30 days ÷ total enrolments, expressed as percentage

Filters

• Default view: current academic year, all faculties

• User-controlled: faculty, programme level (UG/PG), academic year

• Hidden: students with confidentiality flag (handled at SIS row-level security)

Display Rules

• Enrolment-vs-target: **green** if ≥ 95%, **amber** if 85–95%, **red** if < 85%

• Faculties below target appear at top of the list (sort by % ascending)

• Withdrawal rate flagged if > 5%, with link to detail report

PERMISSIONS AND TEST RESULTS

USER PERMISSIONS

ROLE / GROUP	ACCESS LEVEL	MECHANISM
Faculty Deans (8 people)	View their faculty	AD group `FacultyDeans`
Associate Deans (24 people)	View their faculty	AD group `AssocDeans`
DVC Education + 2 reports	View all faculties	AD group `DVCEd_Office`
Academic Ops Admins (3)	Edit + view all	AD group `AcadOps_Admin`

Row-level security applied via faculty_id from SIS — ensures Deans only see their faculty.
All access by AD group, not by individual — joiners/leavers handled by HR processes.

TEST RESULTS

CRITERION	RESULT	TESTED ON
1.1 Daily refresh by 06:00	**PASS**	14 April 2026
1.2 Faculty filter applies	**PASS**	14 April 2026
2.1 RAG colours correct	**PASS**	14 April 2026
2.2 Withdrawal rate displays	**PASS**	14 April 2026
3.1 Confidentiality flag honoured	**PASS**	15 April 2026

CONFIGURATION SIGN-OFF

Implementer: Priya Sharma — BI Specialist, Academic Operations 15 April 2026 *[P. Sharma]*

"This guide accurately describes the configuration deployed."

USER-FACING DOCUMENTATION

SECTION 1 — QUICK-START USER GUIDE

One-page guide showing how to use the result. Screenshots if helpful.

Step 1. Access
Where do I find it? How do I log in?

Step 2. First view
What I see when I open it. What each part means.

Step 3. Common tasks
2–3 most common things a user will do, with screenshots.

Step 4. What if something looks wrong?
Where to look first. Who to call.

Should fit on one printed page or single screen scroll.
Written for the actual user, not for the implementer.

SECTION 2 — KNOWN LIMITATIONS

What this does NOT do, by design. Prevents users raising tickets for things that are intentional rather than defects.

Limitation 1

_____

Limitation 2

_____

Limitation 3

_____

"By design" framing — distinguishes intentional from defect.

SUPPORT AND CLOSURE

SECTION 3 — SUPPORT CONTACTS

Named individuals, not generic email addresses.

ISSUE TYPE	PRIMARY CONTACT	METHOD
Data issues	_____	_____
Access issues	_____	_____
Functional questions	_____	_____
Out-of-hours / urgent	_____	_____

Each contact has a backup. Escalation path documented.

SECTION 4 — TWO-WEEK USAGE REVIEW

Scheduled review point two weeks after launch.

Review date _____

Attendees Business owner, key users, implementer, analyst

Agenda

- Adoption check against success criteria
- Defects raised, status, resolution
- Change requests — captured as new initiatives
- Lessons captured

CLOSURE NOTE — ONE PARAGRAPH AFTER REVIEW

Drafted by Analyst · Approved by Business Owner
"What was delivered, against what success criteria, with what measured outcome at two weeks."

USER-FACING DOCUMENTATION

QUICK-START USER GUIDE — FOR REQUESTORS

Step 1. Find your request

Open **`records.gov.au/track`** in your browser. Enter your reference number (e.g. `RR-2026-12345`) and the email address used to lodge the request.

Step 2. Read the status

You will see one of five statuses:

- **Received** — we have your request
- **Under review** — assessing scope and exemptions
- **Information requested** — we need more from you (action required)
- **Decision pending** — at the decision-maker's desk
- **Completed** — outcome letter sent

Step 3. Action requests

If status is **Information requested**, click "Reply" to upload documents or send additional information directly through the portal.

Step 4. If something looks wrong

Call 1800 RECORDS (1800 732 673) Mon–Fri 9am–5pm AEST.

KNOWN LIMITATIONS — BY DESIGN

L1. Status updates within 24 hours, not real-time

Status changes are pushed to the portal once daily at 2am. A user who reads the status at 10am may see information up to 8 hours old. Real-time updates deferred to FY27 if the cost is justified.

L2. Bulk requests show summary status only

Requests with multiple records show overall status. Per-record status would have required core records-system change — out of scope for this initiative.

L3. No mobile app — browser only

Mobile-responsive web only. Native app rejected on cost-benefit at this stage.

Tested on iOS Safari and Android Chrome — works without scrolling on standard phones.

SUPPORT AND CLOSURE

SUPPORT CONTACTS

ISSUE TYPE	PRIMARY CONTACT	METHOD
Data issues (status mismatch)	Tom Walsh, Records Ops	Service desk + flag
Access / login issues	IT Service Desk Tier 2	x4500 / portal
Functional questions	Sarah Connor, Records BA	Direct email
Out-of-hours / urgent	Duty Records Officer	On-call rota

Backups: Tom → James Park · Sarah → Alex Chen · Records Ops daytime: David Lim.
Escalation: Director of Records (after 24 hours unresolved).

TWO-WEEK USAGE REVIEW

Review date 14 May 2026, 10:00–10:45 AEST · Records Ops Meeting Room 2 + Teams

Attendees Director of Records (Sponsor) · Records Ops Manager · 2 Records Officers · Implementer · Sarah Connor (Analyst)

Pre-review metrics
Distinct portal users (target 200/wk): **274**
Inbound enquiry calls (baseline 580/wk): **418 (–28%)**
Defects raised: **3 (1 fixed, 2 backlog)**
Change requests raised: **5 (transferred to FY27 list)**

Adoption already exceeded the 4-week target by week 2.

CLOSURE NOTE

"Status portal launched 30 April 2026, on schedule. At 14-day review: 274 weekly users (137% of target), enquiry calls reduced 28%, three success criteria fully met, two partially. Initiative formally closed."

Approved: Director of Records, 14 May 2026

WHY INVEST

SECTION 1 — STRATEGIC ALIGNMENT

How the initiative supports stated organisational strategy.

Reference specific strategic plan goals — not abstract ambitions.

_____

_____

_____

SECTION 2 — VALUE PROPOSITION

The quantified benefit. Drawn from the Desired Outcome and the To-Be design.

Annual benefit $_____ (cost savings + revenue + risk reduction)

Payback period _____ months from go-live

NPV (3 years) $_____ at __% discount rate

Key assumptions _____

Sensitivity analysis on key assumptions in supporting workbook.

SECTION 3 — INVESTMENT SUMMARY

Build cost $_____ (one-off)

Annual run cost $_____ (operating)

Timeline _____ months from approval to go-live

Key dependencies _____

Reconciles to portfolio finance norms; capex/opex split confirmed with finance.

OPTIONS, RISK, AND APPROVAL

SECTION 4 — OPTIONS ANALYSIS

At least three options considered. Recommendation made with reasoning.

OPTION	COST / VALUE	DECISION
Do nothing	$0 / declining	_____
Lighter alternative	_____	_____
Recommended option	_____	_____

Rationale captured in supporting paper. "Do nothing" always considered.

SECTION 5 — RISK AND MITIGATION (TOP 5)

For each risk: description, likelihood, impact, mitigation, owner.

R1. _____

R2. _____

R3. _____

R4. _____

R5. _____

SECTION 6 — APPROVAL

Sponsor: _____ · Date: _____ · Signature: _____

CFO: _____ · Date: _____ · Signature: _____

Portfolio governance forum: _____ · Decision recorded in minutes

WHY INVEST

STRATEGIC ALIGNMENT

Supports two FY26–FY28 strategic plan goals:

- **"Customer experience leadership"** — claims journey is the highest-impact customer touchpoint and currently scores 62% (industry: 78%).
- **"Operational efficiency through automation"** — manual triage consumes $6.1M of staff effort annually; automatable to 60–65% with current technology.

Cross-checked with Strategy Office, 18 May 2026.

VALUE PROPOSITION

Annual benefit **$3.4M** ($2.1M cost savings, $0.8M reduced rework, $0.5M customer retention)

Payback period **14 months** from go-live

NPV (3 years) **$5.8M** at 8% discount rate · IRR 42%

Key assumptions

Straight-through processing reaches 60% by month 12 (currently 0%)
Tier 1 attrition continues at current rate (~12% annually); no redundancies

Sensitivity: NPV remains positive at 40% straight-through (downside scenario).

INVESTMENT SUMMARY

Build cost **$1.85M** ($1.4M build, $0.3M vendor licenses Yr 1, $0.15M change mgmt)

Annual run cost **$340k** (licenses + cloud hosting + 1 FTE Triage Operations Analyst)

Timeline **9 months** (Mar 2026 approval → Dec 2026 production go-live)

Key dependencies

Vendor AI Vision Service contract (signed) · Member Portal v2 release (Q3 2026)

Capex/opex: $1.4M capex, $0.45M opex Yr 1 — confirmed with Finance 22 May.

OPTIONS, RISK, AND APPROVAL

OPTIONS ANALYSIS

OPTION	COST / 3-YR VALUE	DECISION
Do nothing	$0 / decline 4–6%	Rejected
Vendor SaaS only (no integration)	$0.9M / $1.6M NPV	Rejected
Custom build (in-house)	$3.2M / $4.1M NPV	Rejected
Hybrid (vendor + integration)	**$1.85M / $5.8M NPV**	**Recommended**

Hybrid balances time-to-value with control. Full options paper attached.

TOP 5 RISKS AND MITIGATIONS

R1. Vendor AI Vision SLA breach High likelihood, medium impact
Mitigation: contract with credit clauses; on-prem fallback. Owner: CIO.

R2. Straight-through rate < target (60%) Medium likelihood, high impact
Mitigation: phased rollout; tune rules monthly. Owner: COO.

R3. Tier 1 staff disengagement Medium likelihood, medium impact
Mitigation: change management plan; transparent communications. Owner: HR.

R4. Member Portal v2 delivery slip Medium likelihood, low impact
Mitigation: dependency tracked weekly with Portal team. Owner: PM.

R5. Regulatory change in claims handling Low likelihood, high impact
Mitigation: configurable rule engine; legal liaison monthly. Owner: Compliance.

APPROVAL

Sponsor: David Chen — Chief Operations Officer · 28 May 2026 · *[D. Chen]*

CFO: Patricia Wong — Chief Financial Officer · 28 May 2026 · *[P. Wong]*

Approved at Investment Committee, 28 May 2026 — minute IC-2026-019.

WHO MATTERS AND HOW MUCH

SECTION 1 — PERSONA MAPPING (5–10 PERSONAS)

Each persona represents a user group affected by the initiative.

Persona 1 — _____
Goals · Pain points · Behaviour · Estimated population

Persona 2 — _____
Goals · Pain points · Behaviour · Estimated population

Persona 3 — _____
Goals · Pain points · Behaviour · Estimated population

Persona 4 — _____
Goals · Pain points · Behaviour · Estimated population

Personas are roles, not individuals. Use real quotes from interviews.

SECTION 2 — INFLUENCE / SUPPORT MATRIX

Each named stakeholder rated for influence (low/medium/high) and support.

	ADVOCATE	NEUTRAL	BLOCKER
HIGH	*Champion*	*Convince*	*Address urgently*
MEDIUM	*Engage*	*Inform*	*Mitigate*
LOW	*Acknowledge*	*Monitor*	*Monitor*

Place each named stakeholder by influence × support.

COMMUNICATION AND DECISION RIGHTS

SECTION 3 — COMMUNICATION PLAN

Who is communicated to, how often, through what channel, with what message.

AUDIENCE	CADENCE	CHANNEL	OWNER
Executive sponsor	Monthly	1:1 + report	_____
Steering committee	Fortnightly	Meeting + pack	_____
Affected staff (P1)	Weekly	Email + intranet	_____
Affected staff (P2)	Monthly	Town hall	_____
External / customers	At go-live	Comms + portal	_____

Each row has a single named owner. Cadence is realistic, not aspirational.

SECTION 4 — DECISION RIGHTS

Who has final say on what. Surfaces conflicts before delivery, not after.

DECISION TYPE	DECISION MAKER	CONSULTED
Scope changes	_____	_____
Functional design	_____	_____
Go-live readiness	_____	_____
Post-launch changes	_____	_____
Acceptance criteria	_____	_____

Single decision-maker per row. Conflicts resolved before delivery starts.

WHO MATTERS AND HOW MUCH

PERSONA MAPPING (5 PERSONAS)

P1. Frontline Customer Service Agent — Population: ~1,200 across 4 contact centres

Goals: resolve calls in under 6 minutes · Pain: switching between 5 systems · Behaviour: follows scripts but improvises

P2. Team Leader — Population: ~80

Goals: meet team SLAs · Pain: limited real-time view of team · Behaviour: highly resistant to change after 2 prior failed initiatives

P3. Workforce Planner — Population: 6

Goals: optimise rostering · Pain: data lag in current tooling · Behaviour: heavy spreadsheet user, slow to adopt new tools

P4. Customer (B2C) — Population: ~2.4M active

Goals: resolve issue in one contact · Pain: repeating information · Behaviour: 38% of contacts via app, 41% phone, 21% web

P5. Compliance Officer — Population: 12

Goals: audit-ready logs · Pain: gaps in current call recordings · Behaviour: rigorous, detail-driven, low risk tolerance

Personas validated through 18 interviews and 4 contact-centre observations, March 2026.

INFLUENCE / SUPPORT MATRIX — KEY STAKEHOLDERS

	ADVOCATE	NEUTRAL	BLOCKER
HIGH	**D. Tan** (COO, Sponsor) CIO (J. Patel)	L. Ng (Compliance Director)	**M. Ross** (Head of CC Ops) *scarred by past initiatives*
MEDIUM	Workforce Planning team lead (S. Park)	Team Leaders (×80) *mixed - need persuasion*	Senior agents *protective of workflows*
LOW	New hires	External vendors	Legacy IT support

M. Ross is the critical stakeholder to convert — without him the change won't land.

Plan: pair him with CIO at vendor demos. CIO is his peer and a credible advocate.

COMMUNICATION AND DECISION RIGHTS

COMMUNICATION PLAN

AUDIENCE	CADENCE	CHANNEL	OWNER
D. Tan (COO)	Monthly	1:1 + status pack	PM (Diaz)
M. Ross (Head CC)	Fortnightly	Joint with CIO	Sponsor
Steering committee	Fortnightly	Meeting + pack	PM
Team Leaders (×80)	Monthly	Town hall + Q&A	M. Ross
CC agents (~1,200)	Weekly	Intranet + huddles	TLs
Customers	At go-live + 30d	App banner + email	Marketing

M. Ross deliberately gets joint sessions with CIO — peer pressure, not lecture.

DECISION RIGHTS

DECISION TYPE	DECISION MAKER	CONSULTED
Scope changes (> $50k)	D. Tan (Sponsor)	CFO, M. Ross
Functional design	M. Ross (Head CC)	TL forum, BA
Go-live readiness	D. Tan + M. Ross (joint)	CIO, Compliance
Acceptance criteria	M. Ross	BA, Test Lead
Compliance sign-off	L. Ng (Compliance)	Legal, CIO

Single decision-maker per row. M. Ross has more authority than typical to address blocker risk.

FUNCTIONAL AND NON-FUNCTIONAL

SECTION 1 — FUNCTIONAL REQUIREMENTS

User stories with acceptance criteria, traceable to Desired Outcome and To-Be design.

ID	USER STORY	ACCEPTANCE	TRACES TO
F-01	As a [role], I want…	3 criteria	DO-1
F-02	As a [role], I want…	__ criteria	DO-_
F-03	As a [role], I want…	__ criteria	DO-_
F-04	As a [role], I want…	__ criteria	DO-_
F-05	As a [role], I want…	__ criteria	DO-_

Typical Silver: 15–40 functional requirements. Detailed list as supporting artefact.

Traceability column is non-negotiable. A requirement without a measurable outcome is a wish-list item.

SECTION 2 — NON-FUNCTIONAL REQUIREMENTS

Six categories. Calibrated to enterprise volumes and tolerances.

Performance	Response time, throughput, concurrency under expected load
Security	Authentication, authorisation, encryption, audit logging
Availability	Uptime target, RTO, RPO, planned vs unplanned downtime
Scalability	Growth assumptions over 3–5 years; how the system scales
Accessibility	WCAG level (AA typical); assistive tech support
Supportability	Logging, monitoring, alerting, troubleshooting

All six populated. "Not applicable" stated explicitly where it is.

DATA DEFINITIONS

SECTION 3 — DATA ENTITIES

For each data entity: attributes, ownership, sources, quality requirements.

ENTITY	OWNER	SOURCE OF TRUTH	QUALITY
_____	_____	_____	_____
_____	_____	_____	_____
_____	_____	_____	_____
_____	_____	_____	_____

Owner is named individual at director level or higher. Quality is measurable.

Why ownership matters:
Without a named owner, data quality is no-one's problem. Initiatives discover this in production, not in design.

SECTION 4 — TRACEABILITY MATRIX

Every requirement linked to a measurable outcome from the Project Vision.

REQ ID	DESIRED OUTCOME	MEASURE OF SUCCESS
F-01	_____	_____
F-02	_____	_____
F-03	_____	_____
NF-Perf-01	_____	_____
NF-Avail-01	_____	_____

No requirement without a measurable outcome it serves.

FUNCTIONAL AND NON-FUNCTIONAL

FUNCTIONAL REQUIREMENTS (extract)

ID	USER STORY (summarised)	ACCEPTANCE	TRACES TO
F-01	Patient receives SMS 7d before appt	3 criteria	DO-1, DO-3
F-02	Patient confirms or cancels via reply	4 criteria	DO-1
F-03	System auto-offers cancelled slot to waitlist	3 criteria	DO-2
F-04	Reception sees real-time confirmation status	2 criteria	DO-1, DO-2
F-05	Clinicians flagged of likely no-shows	2 criteria	DO-2
F-06	Multilingual SMS (English, Mandarin, Arabic)	2 criteria	DO-3, DO-4
F-07	Carer / family delegate notification	3 criteria	DO-3

Total: 23 functional requirements (full list in supporting workbook).

All 23 trace to one of the four Desired Outcomes (no orphan requirements).

NON-FUNCTIONAL REQUIREMENTS

Performance	SMS sent within 60 sec; reply processed within 30 sec; 5,000 SMS/hour
Security	Messages contain no clinical detail; PII encrypted at rest (AES-256) and in transit
Availability	99.5% target; RPO 15 min; RTO 4 hours; aligned to Patient Admin SLA
Scalability	Current 12k appts/wk; design for 25k/wk by FY28 (planned new clinics)
Accessibility	WCAG 2.2 AA · TTY support · audio reminder option for visually impaired
Supportability	Centralised logs (Splunk); alerting on SMS gateway failures; runbook in Confluence

All six categories populated with measurable targets calibrated to hospital-system context.

DATA DEFINITIONS

DATA ENTITIES

ENTITY	OWNER	SOURCE OF TRUTH	QUALITY
Patient	CMIO	PAS (Cerner)	99% complete
Appointment	Director OP	Bookings system	100% appts
Contact preference	Privacy Officer	Patient portal	82% known
Carer / delegate	CMIO	Consent register	61% known
Waitlist	Director OP	Bookings system	94% complete

Carer/delegate quality of 61% is a known risk. Pre-launch data uplift project running.

Why ownership matters:
CMIO sign-off needed for any change to Patient or Carer data flow — Privacy Act obligation. Captured here so consent gates are not surprised at design time.

TRACEABILITY MATRIX (extract)

REQ ID	DESIRED OUTCOME	MEASURE OF SUCCESS
F-01	Reduce no-show rate to under 8%	No-show % at month 3
F-03	Reduce wait time by 15%	Median wait at month 6
F-06	CALD groups reach parity	No-show by language
NF-Perf-01	Reminders timely (under 60s)	SLA monthly
NF-Avail-01	Service availability 99.5%	Uptime monthly

All 23 functional and 18 non-functional requirements traced. Zero orphan requirements.

AS-IS PROCESS MODELS

SECTION 1 — AS-IS PROCESS MODELS

Each major process flow with role swim-lanes, system touchpoints, decision points, and pain points annotated. Multiple flows where the scope spans processes.

[Swim-lane process flow with system touchpoints and pain points marked]

Roles down the side, sequential steps left to right, systems shown above each step

SECTION 2 — ROLES & RESPONSIBILITIES (RACI)

For each major activity:

R — Responsible (does the work)

A — Accountable (single named person)

C — Consulted (input before)

I — Informed (notified after)

One Accountable per activity. Multiple Rs OK.

SECTION 3 — DATA SOURCES

For each process step:

- Data entities consumed
- Data entities produced
- Owner system / source of truth
- Format and cadence
- Manual handoffs flagged

Cross-references the As-Is/To-Be Analysis foundation document.

PAIN POINT ANNOTATIONS

Each pain point identified in the As-Is/To-Be Analysis appears on the process model at its actual location — pinned to the specific step where it occurs.

Convention: red-numbered annotations (P1, P2, …) on the diagram, with a key beside the diagram listing each pain point.

TO-BE PROCESS MODELS

SECTION 4 — TO-BE PROCESS MODELS

Future flows at the same depth as As-Is, so they can be compared. Role changes, system changes, and automation introduced are all explicit.

[To-Be swim-lane with new roles, automated steps, and controls marked]

*New steps in **blue** · Automated in light blue · Removed steps shown in grey for reference*

SECTION 5 — SYSTEM INTERACTIONS

How future systems work together at each step:

- APIs invoked, sequence, payload
- Synchronous vs asynchronous
- Error handling and retries
- Where data is mastered

Sufficient detail for a delivery team to estimate from.

SECTION 6 — CONTROLS & MEASURES

Where in the To-Be process measurements are taken and controls applied:

- Operational metric capture points
- Quality control gates
- Compliance checkpoints
- Exception escalation paths

Measures map to Project Vision targets.

SIDE-BY-SIDE COMPARISON


The acid test: a stakeholder looking at As-Is and To-Be side by side should clearly see the improvement.

If they cannot, the To-Be is not yet sharp enough.

Common indicators: same number of steps, same handoffs, same role count — the To-Be has been drawn but not designed.

AS-IS — SME LOAN ORIGINATION TODAY

PROCESS — 17 BUSINESS DAYS MEDIAN, 28 DAYS WORST CASE



P1 = Manual document checklist; P2 = Customer back-and-forth (avg 2.4 cycles); P3 = Manual underwriting

RACI (KEY ACTIVITIES)

ACTIVITY	R	A	C	I
Initial screen	Banker	RM	Cred	—
Doc collection	Banker	Banker	Cust	RM
Compile case	Banker	RM	Risk	—
Credit decision	Cred Ops	Head Cred	Risk	RM
Notify customer	Banker	Banker	—	Cust

5 activities; single A per row.

DATA SOURCES

Loan application form
PDF · email submission · Indexed manually · 16% mis-routed

Financial statements
PDF / scan · 8 doc types · banker re-keys to underwriting template

Credit bureau report
Online lookup · stored in case file · expiry not tracked

Underwriting decision
Spreadsheet template · stored on shared drive · audit trail weak

PAIN POINT KEY

P1 — Manual document checklist (banker)	2.4 hours per application; checklist drift between bankers
P2 — Customer back-and-forth on docs	Avg 2.4 cycles · 6.2 days added to total time
P3 — Manual underwriting decision	3.5 days median · 73% of cases follow standard rules

Pain points map directly to To-Be design opportunities — addressed in Sections 4–6.

TO-BE — TARGET STATE FY27 Q3

PROCESS — 4 BUSINESS DAYS MEDIAN, 9 DAYS WORST CASE



73% straight-through (no banker review). 27% to banker review for exception cases.

SYSTEM INTERACTIONS

Customer Portal → Origination Hub
REST API · synchronous · application JSON · idempotent

Origination Hub → Doc Extract
Async event · S3 + Lambda · OCR + classifier model

Origination Hub → AI Underwriting
Sync REST · vendor SaaS · timeout fallback to manual

All systems → Decision Log
Append-only · immutable · APRA audit trail format

Architecture review signed off 12 June.

CONTROLS & MEASURES

Application time stamp
At each stage; feeds median-cycle KPI

AI confidence threshold
< 0.85 routes to banker; tracked weekly

Override rate ceiling
Banker overrides logged; alert at > 8%

Customer NPS post-decision
In-portal survey; target NPS +35

All map to Project Vision DO targets.

SIDE-BY-SIDE OUTCOME

Median cycle:	17 days → 4 days	(76% reduction)
Banker time per app:	2.4 hrs → 0.4 hrs	(in exceptions only)
Customer cycles:	2.4 → 0.3 avg	(documents extracted automatically)

All three pain points addressed. Side-by-side comparison defensible to sponsor and APRA.

PROCESS AND JOURNEY DESIGN

SECTION 1 — PROCESS FLOWS (BUILDABLE)

Detailed, buildable flows for each user journey. Sufficient depth for a delivery team to estimate from.

[One detailed swim-lane diagram per primary user journey]
Decision points labelled · Exception paths shown · Timing on each step
Cross-reference to Process Models artefact

Typically 3–6 process flows per Silver initiative

More than 8 flows usually means scope is broader than Silver. Re-run Tier Classifier.

SECTION 2 — USER JOURNEYS

End-to-end experience from each persona's perspective.

PERSONA	JOURNEY OUTCOME	TOUCHPOINTS
Persona 1 — _____	_____	__ steps
Persona 2 — _____	_____	__ steps
Persona 3 — _____	_____	__ steps
Persona 4 — _____	_____	__ steps

Each journey shows what the persona sees, does, thinks, and feels at each touchpoint.
Critical pain points and moments of delight marked.

WIREFRAMES AND TECHNICAL OVERVIEW

SECTION 3 — WIREFRAMES / SCREEN CONCEPTS

For each major UI element. Sufficient for a designer to produce visuals and a developer to estimate build.

Screen 1	Screen 2	Screen 3	Screen 4
Login / entry	*Main view*	*Detail / action*	*Confirmation*

Per wireframe:

- Layout · key UI elements · key data fields · primary action
- Validation rules · error states · empty states · loading states
- Accessibility annotations · responsive behaviour

SECTION 4 — TECHNICAL OVERVIEW

High-level architecture. Components, interfaces, data flows. Written for the delivery team to act on.

Components

New: _____
Modified: _____
Existing (no change): _____

Integrations

_____
_____

Hosting / deployment

_____

Architect signs off the technical overview before delivery commences.

PROCESS AND JOURNEY DESIGN

PROCESS FLOWS — 4 PRIMARY JOURNEYS

Flow 1 — Weekly Risk Score Generation

SIS extract → LMS extract → 5-factor model → Risk score → Adviser feed

Flow 2 — Adviser Triage and Outreach

View list → Drill-down → Decide action → Contact → Log in CRM

Flow 3 — Student Self-Service Wellbeing Check

Login → View status → Self-refer

Flow 4 — Cohort Reporting (Faculty)

Filter cohort → View trends → Export report

All four flows detailed in supporting design pack with timing, roles, exception paths.

USER JOURNEYS — END-TO-END EXPERIENCE

PERSONA	JOURNEY OUTCOME	TOUCHPOINTS
Academic Adviser	Identify and contact at-risk students weekly *Email digest → Dashboard → Drill-down → Outreach → Log → Follow-up → Close*	7 steps
Student (at-risk)	Receive support proactively, not after failure *Notification → Adviser email/call → Optional self-service portal → Action → Outcome*	5 steps
Faculty / Dean	Understand cohort risk and intervention impact *Login → Cohort view → Trend analysis → Action plan with student services*	4 steps
Wellbeing Officer	Receive warm handoffs from advisers *Receive referral → Triage → Initial contact → Support plan → Close referral*	5 steps

Each journey co-designed with 3 advisers, 5 students, 1 faculty representative, March 2026.

WIREFRAMES AND TECHNICAL OVERVIEW

SCREEN CONCEPTS — 4 PRIMARY SCREENS



Common annotations across all screens:

- WCAG 2.2 AA · keyboard nav · screen reader · 200% zoom · colour-blind safe
- Privacy: confidentiality flag honoured · audit log on every read of student data
- Mobile-responsive (320–1920px) · offline state for advisers in field

High-fidelity prototypes built in Figma. Tested with 12 advisers, 8 students.

TECHNICAL OVERVIEW

Components

New: Risk Engine (Python, model trained on 5y historical) · Adviser Web App (React)
Modified: Student Portal (new wellbeing tile) · Faculty Reports (new pages)
Existing (no change): SIS, LMS, IDP, CRM

Integrations

SIS → Risk Engine: nightly batch (existing pipeline) · LMS → Risk Engine: nightly delta
Risk Engine → Adviser App: REST (real-time when adviser opens dashboard)
Adviser App → CRM: bi-directional REST for contact logs and referrals

Hosting

Existing university Azure tenancy · production in AU East · disaster recovery in AU South

Architect (Tom Patel) signed off technical overview, 8 May 2026 — referenced in Solution Architecture artefact.

SCHEMA AND OWNERSHIP

SECTION 1 — CONTRACT HEADER

Producer system _____

Consumer system(s) _____

Producer owner Named individual, director or above

Effective from _____ · Version: ____

Owners are people, not teams. A single name signs each version of this contract.

SECTION 2 — SCHEMA DEFINITION

Field-by-field definition of the data being exchanged.

FIELD	TYPE	REQUIRED	CONSTRAINTS	PII / SENSITIVE
field_1	string	Y / N	_____	Y / N
field_2	decimal	Y / N	_____	Y / N
field_3	datetime	Y / N	ISO 8601 UTC	Y / N
field_4	enum	Y / N	Listed values only	Y / N
field_5	_____	Y / N	_____	Y / N

Each field has a stable identifier and a clear, single-meaning definition.
Full schema in supporting JSON Schema or Avro definition file.

SLAs, QUALITY, CHANGE MANAGEMENT

SECTION 3 — SLAs & QUALITY GUARANTEES

What the producer commits to, measurably.

Freshness Latest record no older than: _____

Cadence Real-time / hourly / daily / batch: _____

Completeness Min % populated: ____ for required fields

Accuracy Max error rate: ____ % per field

Availability Uptime target: ____ % · MTTR: ____ hrs

Backfill / replay Lookback window: ____ days

Each SLA is measured in production. Breaches generate alerts to the producer owner.

"Best efforts" is not an SLA. Specify what consumers can rely on.

SECTION 4 — CHANGE MANAGEMENT

How changes to this contract are agreed and notified.

Backwards-compatible changes
New optional fields, new enum values, expanded constraints.
Notice period: ____ days · Notification channel: _____

Breaking changes
Field rename, type change, removal, semantic change.
Notice period: ____ days · Co-signed by all consumer owners

Deprecation
Old version supported for ____ days after new version live

Sign-off
Producer owner: _____ · Consumer owner(s): _____
Data Steward (separate from producer or consumer) co-signs as independent gate.

SCHEMA AND OWNERSHIP

CONTRACT HEADER

Producer system Claims Platform (event topic `claims.lifecycle.v2` on Kafka)

Consumer systems Analytics Warehouse · Fraud Detection · Reinsurance Reporting

Producer owner Mark Reynolds — Director, Claims Platform Engineering

Effective from 15 July 2026 · Version: 2.0 · Supersedes v1.4 (deprecated 30 Sep 2026)

Data Steward (independent gate): Sandra Chen, Enterprise Data Office.

SCHEMA — ClaimsLifecycleEvent v2.0 (extract)

FIELD	TYPE	REQ	CONSTRAINTS	PII / SENSITIVE
`claim_id`	UUIDv4	Y	RFC 4122 format	N (synthetic)
`event_type`	enum	Y	CREATED, REVIEWED, SETTLED, …	N
`event_timestamp`	datetime	Y	ISO 8601, UTC, ms precision	N
`policy_number`	string(20)	Y	^P[0-9]{19}$	Y — PII
`claim_amount`	decimal(12,2)	Y	≥ 0.00, ≤ 99,999,999.99 AUD	Y — sensitive
`claim_type`	enum	Y	MOTOR, HOME, LIFE, HEALTH, …	N
`customer_id`	UUIDv4	Y	RFC 4122 format	N (synthetic)
`decision_outcome`	enum	N (post-decision)	APPROVED, DENIED, PARTIAL	N
`handler_id`	string(8)	N (auto only)	Employee ID format	Y — PII
`jurisdiction`	string(2)	Y	ISO 3166-2 (NSW, VIC, …)	N
`schema_version`	string(5)	Y	"2.0.0" for this contract	N

28 fields total. Full Avro schema in repo: `schemas/claims/lifecycle/v2.0.avsc`

PII handling: policy_number and handler_id encrypted in transit (TLS 1.3) and at rest. Reinsurance consumer receives tokenised policy_number per APRA / Privacy Act obligations.
PII flag drives downstream masking automatically — no consumer-side configuration.

SLAs, QUALITY, CHANGE MANAGEMENT

SLAs & QUALITY GUARANTEES

Freshness Events emitted within 60 sec of claim state change

Cadence Real-time stream · expected ~28k events/day

Completeness 99.9% required fields populated; 100% claim_id and event_type

Accuracy claim_amount reconciled with finance daily; max variance 0.01%

Availability 99.9% uptime · MTTR 2 hours · 24×7 on-call

Backfill / replay 7-day retention on Kafka · 90-day replay via archive bucket

Schema validation Avro Schema Registry enforces at producer; rejected events logged

Breaches > 5 minutes alert Mark Reynolds (PagerDuty). Quarterly SLA review with consumers.
v1.4 freshness was 5 min; v2.0 tightens to 60 sec to enable Fraud real-time scoring.

CHANGE MANAGEMENT

Backwards-compatible changes

New optional fields, new enum values added at end, expanded constraints.
Notice: 14 days · **Channel:** #data-contracts-claims Slack + email to consumer owners

Breaking changes

Field rename, type change, required → optional, enum value removal.
Notice: 90 days · **Procedure:** new major version, parallel run, all consumer owners co-sign

Deprecation

v1.4 supported until 30 Sep 2026 (77 days parallel with v2.0)

Sign-off — v2.0

Producer: Mark Reynolds (Claims Platform) · 8 July 2026 · *[M. Reynolds]*
Consumers: J. Lin (Analytics), R. Patel (Fraud), K. Soh (Reinsurance) · co-signed
Data Steward: Sandra Chen (Enterprise Data) · 8 July 2026 · *[S. Chen]*
All five signatures required before contract takes effect.

STRATEGY AND SCENARIOS

SECTION 1 — TEST STRATEGY

Test types in scope, with proportions and ownership.

TEST TYPE	SCOPE	OWNER	% EFFORT
Unit	Code-level isolation	Developer	_____
Integration	Component to component	Test Lead	_____
Functional / E2E	User scenarios end-to-end	Test Lead	_____
Performance	Load, stress, soak	Performance Eng	_____
Security	Pen test, OWASP top 10	Security Lead	_____
UAT	Business sign-off	Business Owner	_____

SECTION 2 — TEST SCENARIOS (TRACEABLE TO REQUIREMENTS)

For each requirement: scenario(s) that prove it works.

SCENARIO ID	DESCRIPTION	REQ TRACED	PRIORITY
TS-001	_____	F-01	P1
TS-002	_____	F-01	P2
TS-003	_____	F-02	P1
TS-004	_____	NF-Perf	P1
TS-005	_____	NF-Sec	P1

Coverage: every functional and non-functional requirement has at least one scenario.
An untested requirement is a defect waiting to be found in production.

ENTRY / EXIT CRITERIA AND UAT

SECTION 3 — ENTRY / EXIT CRITERIA

Entry to Test

Conditions that must be true before test execution can begin.

- Build deployed to test environment
- Test data loaded; baseline snapshot taken
- Smoke test passes
- Test scripts peer-reviewed

Exit to UAT

Conditions that must be true before UAT can begin.

- 100% of P1 scenarios passed
- ≥ 95% of P2 scenarios passed
- No open severity-1 defects
- Performance NFRs met under target load

SECTION 4 — UAT PLAN

Business owner-led validation. The decision gate before go-live.

Participants

__ named users from production roles · __ from each user persona

Duration & cadence

__ days execution · daily triage · weekly steerco update

Pass criteria

All P1 scenarios pass · No P1 defects open · Business owner signs

Sign-off

Business Owner: _____ · Date: _____
Test Lead: _____ · Date: _____
Sponsor: _____ · Date: _____

UAT sign-off is the gate to go-live. Without it, deployment is not authorised.

STRATEGY AND SCENARIOS

TEST STRATEGY

TEST TYPE	SCOPE	OWNER	% EFFORT
Unit	Pick-routing algorithm, RF gun handlers	Developer	25%
Integration	WMS ↔ RF guns, WMS ↔ TMS, WMS ↔ ERP	Test Lead	20%
Functional / E2E	Order to dispatch, including returns	Test Lead	25%
Performance	Peak: 14k orders/hr, 65 active pickers	Performance Eng	15%
Security	RF gun auth, WMS API endpoints	Security Lead	5%
UAT	Pickers, supervisors, dispatch ops	Site Manager	10%

Total: 100% · Production-like environment used for E2E and Performance.

TEST SCENARIOS — KEY SCENARIOS (8 of 47 shown)

ID	DESCRIPTION	REQ	PRI	STATUS
TS-001	Single-line order picked, packed, despatched	F-01	P1	PASS
TS-002	Multi-line order, items in different zones	F-02	P1	PASS
TS-003	Pick rejection — item out of stock at location	F-03	P1	PASS
TS-004	Returns receipt, putaway, inventory update	F-08	P2	PASS
TS-007	Peak load — 14k orders/hr sustained 4 hours	NF-Perf	P1	PASS
TS-008	RF gun offline — orders queued for replay	NF-Avail	P1	PROGRESS
TS-012	RF gun auth — expired credentials rejected	NF-Sec	P1	PASS
TS-018	WMS <-> ERP nightly stock reconciliation	F-15	P1	PASS

All 47 scenarios trace to a requirement. Coverage: 100% functional, 100% NFR.

ENTRY / EXIT CRITERIA AND UAT

ENTRY / EXIT CRITERIA

Entry to System Test

- Build 3.4.0 deployed to TEST-01 (production-like)
- 14-day test data refreshed (sanitised production extract)
- Smoke suite (12 scenarios) all pass
- All 47 scripts peer-reviewed; defect tracker primed

Exit to UAT (current status as at 14 May 2026)

- 100% P1 scenarios passed (32/32) — **met**
- P2 scenarios: 14/15 passed (93.3% — 1 in progress) — **close**
- No open severity-1 defects (2 sev-2 deferred to post-launch) — **met**
- Performance: 14k orders/hr sustained, latency p99 850ms — **met**

Recommendation: hold UAT entry 3 days for TS-008 closure. Sponsor briefed.

UAT PLAN

Participants

12 named users · 6 pickers (3 from each shift) · 3 supervisors · 2 dispatch ops · 1 site manager

Duration & cadence

10 business days execution · daily standup at 09:00 · weekly steerco Wed 14:00
Planned: 18 May – 1 June 2026 · Buffer week available if needed

Pass criteria

100% P1 UAT scenarios pass (38 scenarios) · No P1 defects open · Site manager signs

Sign-off

Site Manager: David Park (Sydney DC) · Date: _____
Test Lead: Mei Lin (Senior QA Engineer) · Date: _____
Sponsor: COO (David Park reports up) · Date: _____

UAT is the gate to go-live. Without site manager signature, peak season cannot accept this build.

TRAINING PLAN

SECTION 1 — TRAINING AUDIENCES & CONTENT

Tailored programme per audience. Generic training is never adopted.

AUDIENCE	CONTENT	FORMAT	DURATION
End users (P1)	Daily tasks, exception handling	Hands-on workshop	__ hours
End users (P2)	Reporting and analysis features	E-learning + Q&A	__ hours
Team leaders	Admin, reports, escalation	Workshop + drill	__ hours
Support staff	Troubleshooting, common defects	Run-book + shadowing	__ hours
Champions	Train-the-trainer	Intensive + cert	__ days

Champions are typically 1 per ~25 end users. They become first-line peer support.

SECTION 2 — SCHEDULE & ADOPTION TRACKING

Sequenced delivery and post-training competency check.

Wave 1 — Champions

Trained ___ weeks before go-live · cohort size: __

Wave 2 — Pilot site

Trained ___ weeks before go-live · cohort size: __

Wave 3 — Full rollout

Trained 1–2 weeks before each rollout group · total cohort: __

Adoption tracking

Daily active users · % licensed users using core flow · ticket volume by category

"Trained" is not "adopted". Track usage in production, not training attendance.

BENEFITS TRACKING

SECTION 3 — BENEFITS REGISTER

Each benefit from the Business Case tracked through to realisation.

BENEFIT	BASELINE	TARGET	OWNER	REVIEW
B-01	_____	_____	_____	_____
B-02	_____	_____	_____	_____
B-03	_____	_____	_____	_____
B-04	_____	_____	_____	_____


Each benefit owner is named, accountable, and present at quarterly reviews.

No measurement → benefit not realised, regardless of what was claimed.

Benefit categories: Cost savings · Revenue · Risk reduction · Capacity created · Customer experience

SECTION 4 — REALISATION CURVE & REPORTING

Expected realisation profile and the rhythm of benefits reporting.



Adoption typically trails go-live by 3–6 months

Reporting cadence

Monthly to sponsor for first 6 months, quarterly thereafter for 18 months

Closure

Initiative closes when sponsor confirms benefits met (or accepts shortfall)

TRAINING PLAN

TRAINING AUDIENCES & CONTENT

AUDIENCE	CONTENT	FORMAT	DURATION
Branch staff (~640)	Digital handoff, exception flows, KYC	Workshop + sim	3 hrs
Relationship Managers (~95)	Co-pilot use, customer journey, escalation	Workshop + Q&A	2 hrs
Branch managers (~187)	Reports, exception monitoring, escalation	Workshop + drill	3 hrs
Compliance & risk (~22)	Audit trail, exception review, AML config	Workshop	4 hrs
Contact centre (~280)	Customer self-service support, escalation	E-learning + huddle	2 hrs
Champions (28)	Train-the-trainer, coaching skills	Intensive + cert	2 days

Total: ~1,250 staff trained · 28 champions = ~1 per ~25 frontline staff. Customer-facing scripts in 4 languages.

SCHEDULE & ADOPTION TRACKING

Wave 1 — Champions

Trained 4 weeks before pilot · 28 people · 14–15 Sep 2026

Wave 2 — Pilot (12 branches, 1 RM team, 1 contact-centre cell)

Trained 2 weeks before pilot go-live · ~95 staff · 5–9 Oct 2026 · pilot live 19 Oct

Wave 3 — Full rollout (175 branches, all RMs, all contact centres)

Sequenced across Nov 2026 – Jan 2027 · ~1,125 staff · regional cohorts of ~120

Adoption tracking — measured weekly from go-live

% of new accounts via digital flow · % branch staff using co-pilot weekly · ticket volume by issue type
Staff confidence score (post-training survey at 2 weeks) · target ≥ 4.0/5

"Trained" measured at week 0; "adopted" measured at week 4. Gap analysis at week 6 if > 15%.

BENEFITS TRACKING


BENEFITS REGISTER (FROM BUSINESS CASE)

BENEFIT	BASELINE	TARGET	OWNER	REVIEW
B-01 Onboard time	4–7 days	<10 min	M. Johnson (Cust Ops)	monthly to M+12
B-02 Drop-off rate	40%	< 8%	M. Johnson (Cust Ops)	monthly to M+12
B-03 Branch data entry	35–40%	< 10%	J. Smith (Head Retail)	quarterly to M+18
B-04 Cost per account	$84	$58	P. Patel (Finance)	monthly to M+24
B-05 Net new accts	today's run-rate	+40%	J. Smith (Head Retail)	monthly to M+24
B-06 Compliance SLA	200–300 backlog	95% < 30m	S. Lee (Risk & Comp)	monthly to M+12

All six benefits trace back to Project Vision Measures of Success and Business Case quantified value.

Categories represented: Cost savings (B-03, B-04) · Revenue (B-05) · Customer experience (B-01, B-02) · Risk (B-06)

REALISATION PROFILE & REPORTING



Reporting cadence

Monthly status to Sponsor (J. Smith) M+0 to M+12 · Quarterly thereafter to M+24

Closure decision

Initiative formally closes M+24 once Sponsor confirms benefits realised or accepts shortfall.

Closure note signed off by Sponsor and added to Benefits Realisation Plan archive.

STRATEGIC THESIS AND ECONOMIC CASE

SECTION 1 — STRATEGIC THESIS

The market shift, regulatory change, or capability gap that demands enterprise-scale response.

Why now? Why this scale? Why this organisation?

_____

_____

_____

SECTION 2 — ECONOMIC CASE (5-YEAR HORIZON)

Total investment $_____ · capex / opex split confirmed with CFO

Annual benefit (Year 5 run-rate) $_____

5-year NPV $_____ at __% discount rate · IRR ____%

Payback period _____ months from go-live (cumulative net cashflow positive)

Sensitivity P10–P90 range modelled; worst-case NPV: $_____; best-case: $_____

Cost of inaction $_____ over 5 years (revenue at risk + cost growth)

Independent CFO office review attached. Monte Carlo simulation in supporting workbook.

SECTION 3 — CAPABILITY VIEW

New or transformed organisational capabilities the programme delivers.

- Capability 1 — current state, target state, business meaning
- Capability 2 — current state, target state, business meaning
- Capability 3 — current state, target state, business meaning

PROGRAMME, RISK, AND APPROVAL

SECTION 4 — PROGRAMME STRUCTURE

Multi-tranche delivery; benefits realisation profile per tranche.

TRANCHE	SCOPE	DURATION	BENEFIT %
T1 (Foundations)	_____	__ months	__%
T2 (Core build)	_____	__ months	__%
T3 (Scale)	_____	__ months	__%
T4 (Optimise)	_____	__ months	__%

Tranche gates: each gate is a discrete board-level go / no-go.

SECTION 5 — RISK PROFILE (TOP 8 ENTERPRISE RISKS)

Each risk owned at executive level. Mitigation budgeted in the investment.

R1. _____

R2. _____

R3–R8 [Detailed register in supporting paper]

Mitigation budget $_____ included in total investment line

Risk-adjusted NPV $_____ (post-mitigation)

SECTION 6 — BOARD APPROVAL

Programme Sponsor: _____ · CFO: _____ · CEO: _____

Recorded in Board Minute reference: _____

STRATEGIC THESIS AND ECONOMIC CASE

STRATEGIC THESIS

Renewable generation has reached 38% of national supply (up from 12% five years ago) and is projected at 55% by 2030. The current grid was designed for centralised, predictable generation; it cannot accommodate distributed, intermittent supply at this scale without losing reliability.

Why now? Regulator (AER) requires demand-response capability by 2029. Without action, ~$420M annual revenue exposure from non-compliance penalties + customer attrition to retailers with smart features.

ECONOMIC CASE (5-YEAR HORIZON)

Total investment	**$340M**	($210M capex / $130M opex over 5 years; CFO confirmed)
Annual benefit (Year 5)	**$185M**	($95M revenue + $58M cost + $32M risk)
5-year NPV	**$420M**	at 7% discount rate · IRR 28%
Payback period	**38 months**	from go-live (cumulative cashflow positive Q3 FY28)
Sensitivity	P10: $185M NPV · P90: $670M NPV · 87% probability NPV > 0	
Cost of inaction	**$1.6B**	over 5 years (penalties + customer loss + grid instability)

CFO Office reviewed and signed; Monte Carlo (10k iterations) attached as appendix C.

CAPABILITY VIEW

- **Real-time grid sensing** — Today: 5-min snapshots → Target: sub-second telemetry across 96% of feeders
- **Distributed energy orchestration** — Today: none → Target: 1.4M residential / 8.2k commercial DERs orchestrated
- **Demand response** — Today: manual industrial only → Target: 380MW automated, residential + commercial
- **Predictive asset health** — Today: time-based maintenance → Target: condition-based, ML-driven

PROGRAMME, RISK, AND APPROVAL

PROGRAMME STRUCTURE — 4 TRANCHES

TRANCHE	SCOPE	DURATION	BENEFIT %
T1 Foundations	Telemetry, data platform, security	12 months	5%
T2 Core build	DER orchestration, demand response	18 months	35%
T3 Scale	National rollout, customer enrolment	18 months	45%
T4 Optimise	ML, predictive maintenance, BAU transfer	12 months	15%

Each tranche gate is a board-level go/no-go. No tranche locked-in until prior delivers.
Cumulative timeline: 60 months · T1 starts Q3 FY26 · T4 closes Q2 FY31.

TOP 8 ENTERPRISE RISKS — EXTRACT

R1. Cyber attack on grid telemetry — High, catastrophic · CISO-owned
Defence-in-depth (zero trust, segmentation, ASD-aligned); $48M mitigation budget allocated.

R2. AER compliance pathway changes mid-flight — Med, high · Regulatory Affairs
Quarterly engagement; contract clauses to permit pivot at tranche gates.

R3. Customer adoption (DER enrolment) below 60% — Med, high · Retail Director
Tariff incentives; pilot by Year 2 to validate; cap T3 spend if < 50% by then.

R4–R8 Workforce capability gap, vendor concentration, weather-driven schedule slip, data privacy, supply-chain disruption — full register Appendix D, scored by ERM.

Mitigation budget: **$67M** included · Risk-adjusted NPV: **$340M**

BOARD APPROVAL


Programme Sponsor: D. Harrison (COO) · CFO: P. Ngu · CEO: M. Foster · Chair: A. Patel *[signed]*

Approved at Board meeting 18 June 2026 · Minute BRD-26-074 · T1 funding released, T2–T4 subject to gates

MAPPING AND GOVERNANCE

SECTION 1 — ENTERPRISE STAKEHOLDER MAP

Internal + external. 30–60 stakeholder groups typi

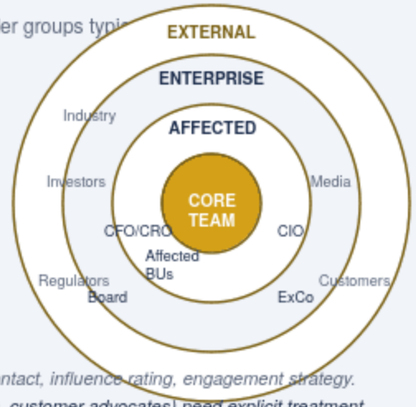

Each stakeholder group has primary contact, influence rating, engagement strategy.
External stakeholders (regulator, media, customer advocates) need explicit treatment.

SECTION 2 — GOVERNANCE STRUCTURE

Multi-tier decision-making aligned to programme tranche gates.

FORUM	DECISIONS	CADENCE	CHAIR
Board	Tranche gates, fund release	Quarterly	Chair
ExCo / Programme Steerco	Cross-BU trade-offs, budget moves	Monthly	Sponsor
Programme Board	Scope, schedule, risk	Fortnightly	Programme Director
Workstream forums	Delivery decisions, dependencies	Weekly	WS Lead
External advisory	Independent challenge, regulator liaison	Quarterly	Chair-appointed

Decision rights matrix in supporting paper. Each forum has terms of reference.

ENGAGEMENT JOURNEY AND COMMS

SECTION 3 — ENGAGEMENT JOURNEY (BY STAKEHOLDER GROUP)

Aware → Understand → Support → Adopt → Advocate. Different groups at different points.

AWARE — knows the programme exists

UNDERSTAND — knows what it means for them

SUPPORT — actively backs the change

ADOPT — uses the new capability daily

ADVOCATE — promotes to peers, defends to detractors

Track each stakeholder group's position quarterly. Plan tactics to move them down the funnel.

SECTION 4 — COMMUNICATIONS STRATEGY

Internal channels
Programme intranet · ExCo updates · BU town halls · all-hands · workstream blogs

External channels
Regulator briefings · investor updates · customer comms · media releases · industry forums

Narrative architecture
Single core narrative · audience-tailored variations · proof points · FAQs maintained


Crisis communications
Pre-positioned holding statements · escalation tree · spokesperson roster

Owner Programme Communications Lead · embedded with Corporate Affairs and Investor Relations

Comms calendar synced to tranche gates and external regulatory milestones.

MAPPING AND GOVERNANCE

STAKEHOLDER MAP — 47 GROUPS IDENTIFIED

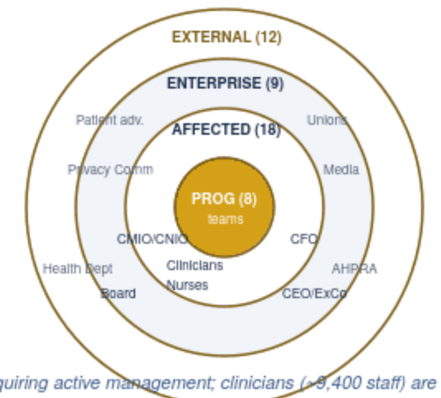

External stakeholders = 12 groups requiring active management; clinicians (~9,400 staff) are the largest affected group.
Clinical unions identified as critical influence — engagement plan separately maintained with HR Director.

GOVERNANCE STRUCTURE

FORUM	DECISIONS	CADENCE	CHAIR
Hospital Board	Tranche gates, $>5M variations	Quarterly	D. Schmidt (Chair)
ExCo Steerco	Cross-hospital trade-offs	Monthly	M. Rao (CEO)
Programme Board	Scope, schedule, risk, vendor	Fortnightly	Programme Director
Clinical Reference Group	Clinical workflow design	Fortnightly	CMIO
Workstream forums (×5)	Build, integration, training, etc.	Weekly	WS Lead
Independent advisory	External challenge, peer review	Quarterly	External Chair

Clinical Reference Group has formal veto on workflow changes — designed in deliberately to prevent EMR failure pattern seen in 5 prior Australian deploym

ENGAGEMENT JOURNEY AND COMMS

ENGAGEMENT POSITION — Q3 FY26 (CURRENT)



Tracked monthly via stakeholder pulse survey · Programme Communications Lead reports to ExCo.

COMMUNICATIONS STRATEGY

Internal channels
Programme intranet (weekly) · CMIO clinical bulletins (monthly) · 8 hospital town halls · workstream blogs

External channels
Health Dept quarterly briefings · Privacy Commissioner annual report · patient newsletter · media holding

Narrative
"Better information at the bedside" — clinician-led, patient-safety framed (not cost-led)

Crisis
Pre-positioned statements for: data breach, go-live disruption, patient safety event, vendor failure

Owner L. Rivera, Programme Comms Lead — embedded with Corporate Affairs & Health Dept liaison

Comms calendar published 24 months ahead and synced to tranche gates and clinical year (Jan/Jul rotations).

CAPABILITY AND PROCESS LANDSCAPE

SECTION 1 — CAPABILITY MAP (HEAT-MAPPED)

Each business capability rated for current performance (red / amber / green).

Capability A1 _____	**Capability A2**	**Capability A3**	**Capability A4**
Capability B1	**Capability B2**	**Capability B3**	**Capability B4**
Capability C1	**Capability C2**	**Capability C3**	**Capability C4**

12+ capabilities typical at Gold scale. Each colour-coded against business outcome metric.

Heat-map answers: where is the organisation weakest, and which capabilities does this programme transform?

SECTION 2 — PROCESS LANDSCAPE

Top-level process taxonomy. Each L1 process decomposes to L2/L3 in supporting model.

L1 PROCESS	VOLUME / FREQUENCY	CYCLE TIME	PAIN POINTS
P-1 _____	_____	_____	__
P-2 _____	_____	_____	__
P-3 _____	_____	_____	__
P-4 _____	_____	_____	__
P-5 _____	_____	_____	__

10–15 L1 processes typical · L2/L3 decomposition in supporting Visio / ARIS pack

SYSTEM AND DATA INVENTORY

SECTION 3 — SYSTEM INVENTORY (CORE)

Systems within scope. Tier classification drives change planning.

SYSTEM	TIER	TECHNOLOGY	END OF LIFE
_____	T1	_____	_____
_____	T1	_____	_____
_____	T2	_____	_____
_____	T2	_____	_____
_____	T3	_____	_____

Tier 1 = mission-critical · Tier 2 = important · Tier 3 = supporting · 50–200 systems typical at Gold scale

EOL surfaces inherent obsolescence: a system at EOL inside the programme window is implicit pressure to replace.

SECTION 4 — DATA & RISK CONTEXT

Data domains

Customer · Employee · Product · Finance · Operations · Compliance · External

Master data state

Per domain: source of truth, completeness, ownership, last reconciled

Regulatory obligations in scope

Privacy Act · industry-specific regulations · APRA / ASIC / etc · cross-border data

Operational risk register tie-in

Existing top risks impacted by programme; new risks introduced; risks mitigated

Cyber posture

Maturity rating (e.g., ASD Essential 8) · current and target · transition plan in scope

Programme inherits these obligations — they do not pause for delivery.

CAPABILITY AND PROCESS LANDSCAPE

CAPABILITY HEATMAP — 12 CAPABILITIES, 3 DOMAINS

CUSTOMER ACQUISITION & RETENTION

Digital onboarding Activation 78% · 4d cycle Industry: 96% · 1d	**Plan management** Self-service 42% Industry: 78%	**Service activation** Same-day 11% Industry: 65%	**Loyalty programmes** Engagement 71% Industry: 67%

SERVICE OPERATIONS

Network ops MTTR 4.2h Industry: 1.8h	**Customer support** FCR 61% Industry: 78%	**Billing** Accuracy 99.7% Industry: 99.4%	**Fraud detection** Coverage 73% Industry: 89%

ENTERPRISE FUNCTIONS

Finance & accounting Stable	**Workforce planning** Manual scheduling	**Data & analytics** Multiple data sources	**Procurement** Stable

5 capabilities red, 5 amber, 4 green. Programme targets the 5 red capabilities — biggest gap to industry.

PROCESS LANDSCAPE — TOP 5 OF 14 L1 PROCESSES

L1 PROCESS	VOLUME / FREQUENCY	CYCLE TIME	PAIN POINTS
P-1 New customer onboard	~480k / year	4 days median	12 (P1)
P-2 Service incident resolve	~22k / month	4.2 hrs MTTR	9 (P1)
P-3 Plan change	~85k / month	2 days median	5 (P2)
P-4 Billing query	~140k / month	18 min avg	4 (P2)
P-5 Customer offboard	~62k / month	19 min avg	2 (P3)

Top 14 L1 processes detailed in supporting ARIS pack. P-1 and P-2 are the programme's lifting agents.

SYSTEM AND DATA INVENTORY

CORE SYSTEM INVENTORY (12 OF 87 IN SCOPE)

SYSTEM	TIER	TECHNOLOGY	END OF LIFE
Customer Mgmt (CMS)	T1	Siebel 8.1 on-prem	Vendor 2027
Order Management	T1	Custom Java 2014	No vendor support
Network Management	T1	HP NNM	2030
Billing & Revenue	T1	Amdocs CES 11	2031
Contact Centre Suite	T2	Genesys on-prem	2028
Data Warehouse	T2	Teradata	2030
Workforce Mgmt	T3	SAP SuccessFactors	SaaS

3 of 4 T1 systems past or near end-of-life — programme implicitly accelerates obsolete platform retirement.

DATA & RISK CONTEXT

Data domains

Customer · Product · Network · Billing · Workforce · Compliance · External (regulator, supplier)

Master data state

Customer 89% · Product 76% · Network 94% · Billing 99% · Workforce 81% — Customer most fragmented

Regulatory obligations

Privacy Act · Telco Consumer Protection Code · ACMA reporting · CDR (Open Telco from 2027)

Cyber posture

ASD Essential 8 maturity 2/3 (target 3/3 by Year 2) · 2023 incident remediation in flight

Top operational risks tied to programme

R-OP-04 Customer churn · R-OP-09 Cyber breach · R-OP-12 Workforce capability gap

Programme inherits regulator deadlines (CDR 2027) — these become hard programme dependencies.

TARGET CAPABILITY AND PROCESS

SECTION 1 — TARGET CAPABILITY MAP

Same structure as As-Is, target state. The arrows are the programme's value generation.

Target FY+5 — colour shows expected position

Capability A1 (now red) Target _____	**Capability A2**	**Capability A3**	**Capability A4** Out of programme scope
Capability B1	**Capability B2**	**Capability B3**	**Capability B4**
Capability C1	**Capability C2**	**Capability C3**	**Capability C4**

Most red and amber capabilities promoted to green by programme close. Out-of-scope capabilities flagged.

"Promote to green" claim must be defensible against measurable benchmarks.

SECTION 2 — TARGET PROCESS LANDSCAPE

Future-state cycle times and degree of automation per L1 process.

L1 PROCESS	CURRENT	TARGET	% AUTO	FTE IMPACT
P-1 _____	_____	_____	__%	_____
P-2 _____	_____	_____	__%	_____
P-3 _____	_____	_____	__%	_____
P-4 _____	_____	_____	__%	_____
P-5 _____	_____	_____	__%	_____

FTE impact: net redeploy / reduce / hire — defensible to HR and unions before approval.

TARGET ARCHITECTURE AND OPERATING MODEL

SECTION 3 — TARGET ARCHITECTURE

Replace · refactor · retain · retire decisions for each Tier 1 system.

DOMAIN	DECISION	TARGET	TRANCHE
_____	Replace	_____	__
_____	Refactor	_____	__
_____	Retain	_____	__
_____	Retire	_____	__

Architecture principles

Cloud-first (where compliant) · API-led integration · Event-driven where latency demands it
Open standards · Single source of truth per data domain · Zero trust security

CTO and Enterprise Architecture forum signed off architecture principles before scope finalised.

SECTION 4 — OPERATING MODEL IMPLICATIONS

Roles changed

Existing roles whose nature changes (skills, accountabilities, reporting).

Roles created

New roles required by future state (e.g., Data Steward, Site Reliability Engineer).

Roles retired

Roles where work is automated away or replaced. Net workforce impact stated.

Decision rights

Where authority shifts (e.g., centralised → federated; tactical → strategic).

Performance metrics

New KPIs introduced; existing KPIs adjusted to reflect future state.

CHRO and union representatives consulted on operating model implications before sign-off.

TARGET CAPABILITY AND PROCESS

TARGET CAPABILITY MAP — FY+5

CUSTOMER & ORIGINATION

Digital onboarding Was red · 4d → 6 min	**Loan origination** Was red · 17d → 4d	**KYC & AML** Was amber · 99% STP	**CX measurement** Real-time NPS

PRODUCT & PRICING

Product launch Was red · 9mo → 6wk	**Personalisation** Was red · ML-driven	**Pricing & offers** Real-time engine	**Product simplification** Out of scope (BU)

RISK & OPERATIONS

Real-time risk Was red · < 1s decisions	**Fraud detection** Was amber	**Reg reporting** APRA / AUSTRAC auto	**Cyber resilience** E8 maturity 3

11 of 12 capabilities to green by FY+5. Product simplification stays amber (separate BU programme).

TARGET PROCESS LANDSCAPE — TOP 5 PROCESSES

L1 PROCESS	CURRENT	TARGET	% AUTO	FTE IMPACT
P-1 SME loan origination	17 days	4 days	73%	−42 redeploy
P-2 New-to-bank onboard	4 days	6 min	94%	−87 redeploy
P-3 Mortgage approval	28 days	8 days	58%	−24 redeploy
P-4 Product launch (E2E)	9 months	6 weeks	N/A	+12 hire
P-5 Reg reporting (APRA)	5 days/qtr	Same-day	88%	−6 redeploy

Net workforce: −147 redeploy + 12 hire = −135 FTE. Reskilling pathway agreed with FSU before sign-off.

TARGET ARCHITECTURE AND OPERATING MODEL

TARGET ARCHITECTURE — TIER 1 SYSTEMS

DOMAIN	DECISION	TARGET	TRANCHE
Core deposits	**Replace**	Vendor cloud-native (Temenos)	T2–T3
Core lending	**Replace**	Same vendor stack	T3
Customer 360	**Refactor**	Cloud-native rebuild on event mesh	T1–T2
Risk & compliance	**Refactor**	Real-time decisioning platform	T2
Channels (digital)	**Retain**	Existing platform, API enhanced	T1
Legacy GL bridge	Retire	Decommissioned post-migration	T4

Architecture principles

Cloud-first (APRA CPS 234 + 230 compliant) · API-led · Event-driven for real-time risk
Open Banking standards · Single golden source per domain · Zero trust security

OPERATING MODEL IMPLICATIONS

Roles changed (~870 staff)

Bankers: more advisory, less data entry · Credit officers: exception focus, less standard work

Roles created (~85 roles)

Data Stewards (12) · SREs (24) · ML Engineers (18) · Product Managers (15) · DevSecOps (16)

Roles retired (~135 FTE)

Manual underwriting, manual reconciliation, manual reg-pack assembly · 100% reskilling pathway

Decision rights

Pricing: tactical → real-time engine · Credit: rule-based → AI with banker exception

Performance metrics

New: Cycle-to-decision, STP %, model accuracy · Retired: manual queue length

CHRO and Finance Sector Union (FSU) reps consulted June 2026; reskilling pathway and severance terms agreed.

REQUIREMENTS HIERARCHY AND DOMAINS

SECTION 1 — REQUIREMENTS HIERARCHY

Outcomes → Capabilities → Features → Requirements. Programme-scale needs structure.



Each level traces to the level above. Gold programmes typically have 300–800 detailed requirements.

SECTION 2 — REQUIREMENTS BY DOMAIN

Volume per domain. Cross-domain dependencies highlighted.

DOMAIN	CAPABILITIES	REQUIREMENTS	CROSS-DOMAIN
Customer	__	__	__
Product	__	__	__
Operations	__	__	__
Risk & Compliance	__	__	__
Data & Analytics	__	__	__

Cross-domain count flags the integration risk profile — high counts mean integration testing is critical.

REGULATORY MAPPING AND NFR

SECTION 3 — REGULATORY MAPPING

Each obligation traces to specific requirements that fulfil it.

REGULATION	CLAUSE	REQUIREMENTS	REGULATOR SIGN-OFF
_____	_____	__ reqs	_____
_____	_____	__ reqs	_____
_____	_____	__ reqs	_____
_____	_____	__ reqs	_____
_____	_____	__ reqs	_____

Regulator sign-off scheduled per tranche gate. Compliance dashboard updated weekly.

Why mapping matters: a single missed obligation can collapse a Gold programme.

SECTION 4 — ENTERPRISE NON-FUNCTIONAL REQUIREMENTS

Calibrated to enterprise volumes and regulatory tolerance.


Performance	Sustained throughput at peak: _____ TPS · p99 latency: ____ ms
Availability	Tier 1: ____% · Tier 2: ____% · MTTR ____ min · MTBF ____ months
Security	ASD Essential 8 maturity level ____ · Zero trust · DLP · IAM enterprise-wide
Scalability	5-year growth: ____× volumes · architecture supports without re-platform
Disaster recovery	RTO: ____ min · RPO: ____ min · annual tested · regulator-witnessed
Accessibility	WCAG 2.2 AA enterprise-wide · audited annually

CTO, CISO, and CRO co-sign the enterprise NFR set. Programme tranche gates re-validate.

NFR breach in production is a board-reportable event.

REQUIREMENTS HIERARCHY AND DOMAINS

REQUIREMENTS HIERARCHY — 487 DETAILED REQUIREMENTS

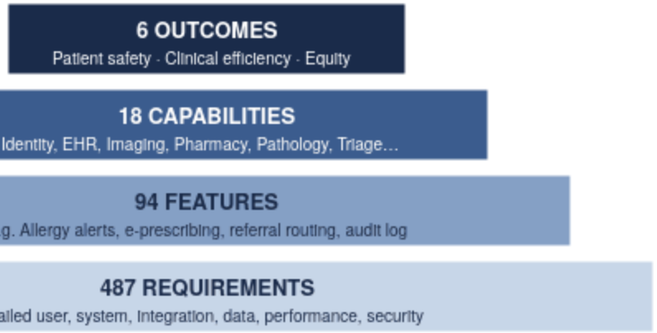

Each level traceable upward and downward in JIRA Align. Quarterly tranche-gate reviews verify completeness and alignment with Outcomes set by the National Health Programme Board.

REQUIREMENTS BY DOMAIN

DOMAIN	CAPABILITIES	REQUIREMENTS	CROSS-DOMAIN
Patient Identity & Access	3	68	**42 (high)**
Clinical Records (EHR)	5	142	**71 (high)**
Pharmacy & Prescribing	3	89	**38 (medium)**
Imaging & Pathology	2	61	**24 (medium)**
Referrals & Care Coordination	2	52	**35 (high)**
Reporting, Analytics & Research	3	75	**28 (medium)**

211 cross-domain requirements (43% of total) — integration testing investment must reflect this.
EHR + Identity domain pair flagged as integration-test critical path.

REGULATORY MAPPING AND NFR

REGULATORY MAPPING — 6 OBLIGATIONS

REGULATION	CLAUSE	REQS	REGULATOR SIGN-OFF
Privacy Act 1988 (APP)	APP 1, 6, 11, 12	94	OAIC — Tranche 2 gate
My Health Records Act	s.59, 70, 75	42	Aust Digital Health Agency
AHPRA Codes (Med, Nurs)	Section 4.5	31	AHPRA Med + Nurs Boards
Therapeutic Goods Act	s.41 (devices)	19	TGA — Class IIa registr.
Notifiable Data Breaches	Part IIIC	14	OAIC — runtime obligation
State health legislation (×8)	Various	37	State health depts

237 of 487 requirements (49%) carry regulatory traceability.
Why mapping matters: a single missed obligation can collapse the programme — and trigger a board-reportable breach.
Regulator sign-off scheduled at every tranche gate.

ENTERPRISE NON-FUNCTIONAL REQUIREMENTS

Performance	Sustained 18,000 TPS at peak (wave 1) · p99 latency < 350 ms · 99.95% APIs
Availability	Tier 1 (clinical): 99.99% · Tier 2 (analytics): 99.5% · MTTR ≤ 30 min · MTBF ≥ 12 months
Security	ASD Essential 8 maturity Level 3 · Zero trust enterprise-wide · DLP · IAM · IRAP assessed
Scalability	5-year growth: 4× volumes (28M → 112M records) · architecture supports without re-platform
Disaster recovery	RTO 60 min · RPO 5 min · annual tested DR exercise · ADHA-witnessed
Accessibility	WCAG 2.2 AA enterprise-wide · audited annually · clinical UX validated by user councils

CTO + CISO + CRO co-signed enterprise NFR set 18 February 2026.
NFR breach in production = board-reportable event.

PROGRAMME REQUIREMENTS SIGN-OFF

CDO: *[Dr. M. Patel]* · CMIO: *[Prof. R. Singh]* · CISO: *[A. Wong]* · CRO: *[K. Daniels]*
Programme Board endorsement: 18 February 2026 · Subject to OAIC + ADHA tranche gates

ARCHITECTURE LAYERS

SECTION 1 — LAYERED ARCHITECTURE

Five-layer model. Each layer contains domains. Patterns documented.

EXPERIENCE / CHANNEL
Customer apps · Staff apps · Partner portals · Voice · Branch · Self-service
Pattern: _____

API / INTEGRATION
API gateway · Service mesh · Event bus · ESB · Pub/Sub · Streaming
Pattern: _____

APPLICATION / DOMAIN SERVICES
Customer · Product · Operations · Risk · Finance · Workforce · Analytics
Pattern: _____

DATA / INFORMATION
OLTP · Data lake · Data warehouse · Master data · Reference data · Real-time
Pattern: _____

INFRASTRUCTURE / PLATFORM
Cloud (region/zone) · Compute · Storage · Network · Identity · Security platform

SECTION 2 — BUILD / BUY / PARTNER DECISIONS

CAPABILITY	DECISION	VENDOR / TECH	RATIONALE
_____	Build/Buy/Partner	_____	_____
_____	Build/Buy/Partner	_____	_____
_____	Build/Buy/Partner	_____	_____

Differentiating capability → Build · Commodity → Buy · Specialist → Partner

NFR FITNESS, RISKS, APPROVAL

SECTION 3 — NFR FITNESS

How the architecture meets each enterprise NFR. Evidence, not assertion.

NFR	TARGET	ARCHITECTURAL APPROACH	EVIDENCE
Performance	_____ TPS	_____	_____
Availability	_____%	_____	_____
Security	Level ___	_____	_____
Scalability	__× growth	_____	_____
DR (RTO/RPO)	__/__min	_____	_____

Evidence options: Load test result · Reference architecture · Vendor benchmark · Pilot result

SECTION 4 — ARCHITECTURAL RISKS

Top 5–8 risks. Each owned by an architect. Mitigation strategy named.

Risk 1. _____
Owner: _____ · Likelihood: ___ · Impact: ___ · Mitigation: _____

Risk 2. _____
Owner: _____ · Likelihood: ___ · Impact: ___ · Mitigation: _____

Risk 3. _____
Owner: _____ · Likelihood: ___ · Impact: ___ · Mitigation: _____

Architectural risks differ from delivery risks: they relate to fitness for purpose, not schedule.

ARCHITECTURE BOARD APPROVAL

Chief Architect: _____ · CTO: _____ · CISO: _____ · CDO: _____
ARB review date: _____ · Conditions: _____ · Re-approval at next major release

ARCHITECTURE LAYERS

LAYERED ARCHITECTURE — FIVE LAYERS

EXPERIENCE / CHANNEL
Customer App (Flutter) · Member Portal (Next.js) · Adjuster Workbench (React) · IVR · Broker Portal · Voice (Genesys)
Pattern: Backend-for-Frontend · Channel-agnostic core API · Design system (Polaris)

API / INTEGRATION
Apigee API gateway · Kafka event bus · Confluent Schema Registry · MuleSoft for legacy bridges
Pattern: Event-driven core · Async by default · Idempotent producers · CDC from legacy

APPLICATION / DOMAIN SERVICES
Claims Lifecycle · Triage AI · Decision Engine · Payments · Fraud · Reinsurance · Customer 360 · Document AI
Pattern: Domain-driven design · One service per domain · Saga for cross-domain transactions

DATA / INFORMATION
PostgreSQL (OLTP per service) · Snowflake (warehouse) · Iceberg lake · Redis (cache) · MDM (Reltio) · ML feature store
Pattern: Data mesh · Domain-owned products · Single source per master entity · Encryption at rest (AES-256)

INFRASTRUCTURE / PLATFORM
AWS (ap-southeast-2 prod, ap-southeast-4 DR) · EKS · Aurora · Terraform IaC · GitHub Actions · Datadog
Pattern: Cloud-native · Zero-trust · Multi-AZ · Multi-region active-passive · IRAP-assessed

BUILD / BUY / PARTNER DECISIONS — TIER 1

CAPABILITY	DECISION	VENDOR / TECH	RATIONALE
Triage AI	**Buy**	Vendor Vision API	Commodity
Claims Decision Engine	**Build**	In-house · Drools rules engine	Differentiating
Fraud detection	**Partner**	FRISS · co-developed models	Specialist
Customer 360 / MDM	**Buy**	Reltio	Commodity
Document AI / OCR	**Buy**	AWS Textract + custom layer	Commodity
Payment orchestration	**Build**	Custom · multi-rail (BPAY, NPP, BECS)	Differentiating

Differentiating → Build · Commodity → Buy · Specialist domain → Partner. ExCo endorsed Q1 FY26.

NFR FITNESS, RISKS, APPROVAL

NFR FITNESS — EVIDENCE-BACKED

NFR	TARGET	APPROACH	EVIDENCE
Performance	5,000 TPS	Horizontal scale, async, sharded	Load test 7,200
Availability	99.95%	Multi-AZ active-active, multi-region DR	DR test passed
Security	Essential 8 L2	Zero trust, IAM, DLP, encrypted everywhere	IRAP report
Scalability	5x growth	Auto-scaling, partitioned data, async	Stress test
Disaster recovery	RTO 30m / RPO 5m	Multi-region, continuous replication	Annual DR drill
Compliance	APRA CPS 234	Continuous monitoring, audit log immutable	APRA audit
Observability	99% trace cov.	OpenTelemetry, distributed tracing, SLOs	Datadog dashboards

Evidence: load test 7,200 TPS sustained 60 min · DR drill 14 May 2026 (28 min RTO actual)
IRAP assessor signed off Aug 2026 · APRA notified per CPS 234 prudential standard

All 7 NFRs evidence-backed before architecture board commitment.

ARCHITECTURAL RISKS — TOP 5

AR1. Vendor lock-in (Vision API) — High likelihood, medium impact
Owner: Chief Architect · Mitigation: standardise model interface, dual vendor pilot in T3

AR2. Saga complexity in cross-domain transactions — Med, high
Owner: Domain Architect · Mitigation: 4-week saga design workshop, formal verification on T1 sagas

AR3. Data mesh ownership maturity — High, medium
Owner: CDO · Mitigation: Data Steward role established for each domain before T2 starts

AR4. Legacy bridge performance degradation — Med, high
Owner: Integration Architect · Mitigation: capacity baselining, sunset triggers in T3

AR5. Multi-region cost overrun — Med, med · Owner: Platform Lead · Mitigation: cost guardrails in IaC, monthly FinOps review

ARCHITECTURE BOARD APPROVAL

Chief Architect: J. Vasquez · CTO: M. Singh · CISO: A. Chen · CDO: P. Walker · ARB date: 22 Aug 2026
Conditions: re-approval at T2 entry · re-approval at major release · half-yearly NFR re-validation

DATA STRATEGY AND DOMAIN MODEL

SECTION 1 — DATA STRATEGY PRINCIPLES

5–8 principles guiding data investment, build, and operation.

P1. Domain ownership — every data product has a single named owner

P2. One source of truth — no parallel masters; CDC for synchronisation

P3. Privacy by design — minimise, anonymise, audit, comply by default

P4. Quality measurable — every domain publishes its own quality metrics

P5. Reuse before rebuild — central catalogue, reuse incentivised

Principles signed off by Data Council and endorsed by ExCo before architecture lock-in.

SECTION 2 — DATA DOMAIN MODEL

Data organised by domain, each with a Domain Steward (director-level).

DOMAIN	PRODUCTS	STEWARD	CLASSIFICATION
Customer / Citizen	__ products	_____	Sensitive PII
Product / Service	__ products	_____	Confidential
Finance	__ products	_____	Restricted
Workforce	__ products	_____	Sensitive PII
Operational	__ products	_____	Internal
Risk & Compliance	__ products	_____	Restricted
External / Reference	__ products	_____	Public / Open

Classification scheme: Public · Internal · Confidential · Restricted · Sensitive PII (highest)

Each level has handling, retention, encryption, and access control rules in supporting standards.

GOVERNANCE, PRIVACY, QUALITY

SECTION 3 — DATA GOVERNANCE FORUMS

FORUM	DECISIONS	CADENCE	CHAIR
Data Council	Strategy, principles, escalation	Quarterly	CDO
Domain Stewards Forum	Cross-domain issues, contracts	Monthly	Head of DG
Privacy Steering	PIA outcomes, breach response	Monthly	Privacy Officer
Data Quality Council	Quality targets, remediation	Monthly	Head of DQ

Each forum has terms of reference, decision rights matrix, escalation path.

SECTION 4 — PRIVACY REGIME

Compliance posture, controls, ongoing assurance.

Frameworks Privacy Act 1988 (APPs) · GDPR (where applicable) · sector-specific (e.g. APRA CPS 234)

Controls PIAs · consent management · data minimisation · DSARs · breach notification (72h)

Assurance Annual external audit · quarterly internal · continuous monitoring (DLP, anomaly)

Privacy Officer reports to CEO; escalates to Board for breaches over threshold.

SECTION 5 — DATA QUALITY REGIME

Measurable, published, attached to compensation in critical domains.

Dimensions: Completeness · Accuracy · Timeliness · Consistency · Validity · Uniqueness

Targets: Per domain, in domain charter; reviewed quarterly by Data Quality Council

Reporting: Monthly DQ scorecard published to all Domain Stewards and ExCo

Critical domains' quality target tied to executive compensation review.

DATA STRATEGY AND DOMAIN MODEL

DATA STRATEGY PRINCIPLES

P1. Citizen consent is paramount — purpose-bound, withdrawable, auditable

P2. Domain ownership — every dataset has a SES Band 1+ Domain Steward

P3. Tell us once — never ask citizens for information already held

P4. Open by default for de-identified data — closed only with documented justification

P5. Data sovereignty — Australian-resident systems for citizen data

P6. Quality before scale — no new use cases until critical-data quality at 95%

Endorsed by Secretary & Senior Executive Service Forum, 14 March 2026 · referenced in Data Strategy 2026–2029.

DATA DOMAIN MODEL — 7 DOMAINS, 184 DATA PRODUCTS

DOMAIN	PRODUCTS	STEWARD	CLASSIFICATION
Citizen Identity	28	FAS Identity Services	PROTECTED
Service Eligibility	42	FAS Service Delivery	SENSITIVE
Payments / Benefits	31	FAS Payments	SENSITIVE
Workforce	19	CHRO	SENSITIVE
Operational / Compliance	26	CRO	RESTRICTED
Public Performance	22	CDO Office	OPEN
Reference / Geospatial	16	Chief Information Officer	PUBLIC / OPEN

Classifications: PUBLIC · OFFICIAL · OFFICIAL: SENSITIVE · PROTECTED · SECRET (per PSPF)

PSPF = Protective Security Policy Framework. Each level: handling, retention, encryption, access rules per ISM (Information Security Manual).

PROTECTED domains require ASD-certified hosting and IRAP-assessed pathways.

GOVERNANCE, PRIVACY, QUALITY

DATA GOVERNANCE FORUMS

FORUM	DECISIONS	CADENCE	CHAIR
Data Council	Strategy, principles, OAIC liaison	Quarterly	CDO
Domain Stewards Forum	Cross-domain rules, contracts, gates	Monthly	Head of DG
Privacy Steering	PIA review, breaches, OAIC reporting	Monthly	Privacy Officer
Data Quality Council	DQ targets, remediation roadmap	Monthly	Head of DQ

Privacy Officer has direct reporting line to Secretary; CDO formally advises Minister.

PRIVACY REGIME

Frameworks Privacy Act 1988 (13 APPs) · Notifiable Data Breaches Scheme · PSPF · ISM · IRAP

Controls PIA mandatory before each new use · consent register · DLP · DSARs · 72-hour OAIC notification

Assurance ANAO biennial · OAIC audit access · IRAP each major release · Senate Estimates

Recent posture: 2 notifiable breaches FY25 (both contained < 24h, OAIC closed); zero in FY26 to date

Privacy Officer reports breach exposure quarterly to Audit Committee; Annual Report disclosed publicly.

DATA QUALITY REGIME

Dimensions: Completeness · Accuracy · Timeliness · Consistency · Validity · Uniqueness · **Provenance**

Targets: Citizen Identity 99% · Service Eligibility 96% · Payments 99.5% · Public Performance 98%

Reporting: Monthly DQ scorecard to ExCo · annual Public Data Quality Statement (transparency obligation)


Recent gap: Service Eligibility currently 89% (target 96% by Q4 FY27) — remediation programme funded $14M

Critical-domain DQ targets attached to SES KPI agreements (precedent set FY25).

TRANCHE PLAN AND GATES

SECTION 1 — MULTI-YEAR SCHEDULE

5-year horizon · 4 tranches · workstream-level visibility.

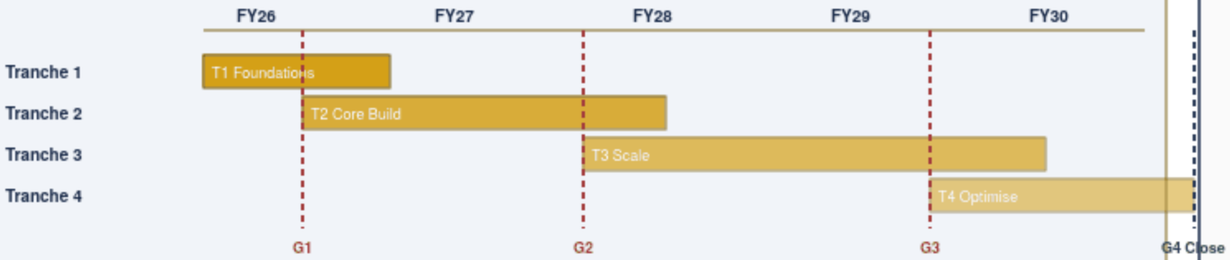

Gate criteria:

G1 — Foundations stable, T2 budget unlocked · G2 — Pilot delivered, T3 funding released
G3 — Scaled rollout proven, T4 commitment · G4 — Programme close, BAU transfer complete

Each gate is a board-level go/no-go decision. No tranche commits until prior delivers.

SECTION 2 — WORKSTREAMS

WORKSTREAM	LEAD	FTE PEAK	PRIMARY TRANCHE
Architecture & design	_____	_____ FTE	T1 + T2
Build & integration	_____	_____ FTE	T2 + T3
Data & migration	_____	_____ FTE	T2 + T3
Change & training	_____	_____ FTE	T3
QA & assurance	_____	_____ FTE	all
Programme office	_____	_____ FTE	all

Workstream lead has hire authority within budget; FTE peak by tranche reviewed quarterly.

DEPENDENCIES, CRITICAL PATH, MILESTONES

SECTION 3 — DEPENDENCIES

Internal and external dependencies that gate delivery.

DEPENDENCY	TYPE	OWNER	REQUIRED BY
Network refresh complete	Internal	_____	_____
Vendor contract execution	External	_____	_____
Regulator approval	External	_____	_____
Workforce ramp	Internal	_____	_____
Data migration window	Internal	_____	_____

Each dependency reviewed weekly · breach triggers escalation to Programme Director within 24 hours.

SECTION 4 — CRITICAL PATH AND MILESTONES

Path that determines minimum delivery time. Slippage on any node delays the programme.

M1. _____
M2. _____
M3. _____
M4. _____
M5. _____
M6. _____


Float / buffer: % slack against schedule, by workstream, reported monthly

Re-baselining: Material variance triggers programme board review and possible re-plan

Critical path published in Programme Board pack monthly; updated when material variance occurs.

TRANCHE PLAN AND GATES

MULTI-YEAR SCHEDULE — JUL 2026 to JUN 2031

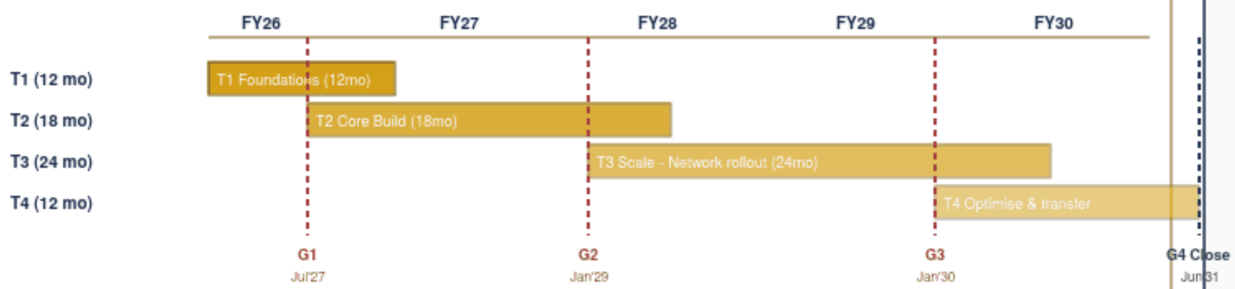

Gate criteria — agreed with ACMA, Board, ExCo:

G1 — Standalone 5G core operating in 2 metros · Spectrum auction won · ACMA milestone met
G2 — 200 sites live, NPS impact measured, vendor SLAs achieved · T3 funding board-approved
G3 — 4G decommission plan ratified · Spectrum reuse confirmed · 2,400 sites operational
G4 — All sites in BAU · 4G core retired · benefits realised · programme team disbanded

Each gate is a board-level go/no-go. T2 budget contingent on G1; T3/T4 contingent on respective predecessors.

WORKSTREAMS — 8 STREAMS, ~340 PEOPLE PEAK

WORKSTREAM	LEAD	FTE PEAK	PRIMARY TRANCHE
Architecture & design	L. Chen (Chief Network Architect)	42 FTE	T1 + T2
Core build (Ericsson)	M. Patel (Head of Core)	88 FTE	T2
Network deployment	D. Walsh (RF Programme)	125 FTE	T3
OSS / BSS integration	J. Singh (Head OSS)	36 FTE	T2 + T3
Cyber & security	A. Hassan (Network CISO)	22 FTE	all
Customer migration	S. Lee (Customer Ops)	18 FTE	T3 + T4
QA / Test / NFR	P. Tran (Senior QA Director)	28 FTE	all
Programme office	R. Mehta (PD)	14 FTE	all

DEPENDENCIES, CRITICAL PATH, MILESTONES

DEPENDENCIES — KEY GATING ITEMS

DEPENDENCY	TYPE	OWNER	REQ BY
Spectrum auction (3.5GHz)	External	ACMA / Govt Affairs	Q4 FY26
Ericsson MSA execution	External	CFO / Procurement	Q3 FY26
Tower co. site agreements	External	Property / Legal	Q4 FY27
Engineering hire ramp (180)	Internal	CHRO / Talent	Q2 FY27
Data centre fit-out	Internal	CIO Infra	Q1 FY27
OSS/BSS data migration window	Internal	CTO / Data	Q3 FY28
CISC compliance assurance	External	CISO / Govt Aff.	Pre-G1 + ongoing

External dependencies tracked weekly · breach escalates to Programme Director within 24 hours.

CRITICAL PATH AND KEY MILESTONES

M1. Q3 FY26 — Ericsson MSA executed; spectrum auction submitted

M2. Q4 FY26 — Spectrum allocation confirmed; T1 architecture frozen; Sydney + Melbourne core lab live

M3. Q2 FY27 — Engineering ramp at 90%; Sydney metro 5G core operational (alpha service)

M4. Q4 FY27 — G1 gate · 2 metros operating; ACMA progress milestone met; T2 funded

M5. Q3 FY28 — 200 sites in production; vendor SLAs achieved; OSS/BSS migration complete

M6. Q2 FY29 — G2 gate · NPS uplift measurable; T3 board-approved

M7. Q4 FY30 — G3 gate · 2,400 sites operational; 4G decommission plan executed

M8. Q4 FY31 — G4 close · BAU transfer complete; programme disbanded; benefits validated

Float / buffer: Currently 12 weeks float in T2 critical path; reported monthly on Programme Board pack

Re-baselining: Variance >6 weeks triggers Programme Board review and possible re-plan; ACMA notified at threshold

Critical path reviewed monthly with Programme Board; spectrum/CISC compliance items remain principal risks.

QUALITY LAYERS AND STRATEGY

SECTION 1 — QUALITY PYRAMID (8 LAYERS)

Each layer has owner, automation level, and evidence captured.

- **L8 · BUSINESS ACCEPTANCE** — Sponsor / Business Owner sign-off · 100% manual
- **L7 · OPERATIONAL READINESS** — Production readiness review · 80% checklist-driven
- **L6 · INDEPENDENT ASSURANCE** — External auditor / regulator · Cyclical
- **L5 · NON-FUNCTIONAL TEST** — Performance, security, DR, accessibility · 75% automated
- **L4 · END-TO-END FUNCTIONAL** — Cross-system journeys · 80% automated
- **L3 · INTEGRATION TEST** — Service-to-service, contract test · 95% automated
- **L2 · COMPONENT TEST** — Per service/module · 100% automated
- **L1 · UNIT TEST** — Code-level, in pipeline · 100% automated

Pyramid principle: more tests at lower layers, fewer at higher. Inverted pyramid is anti-pattern.

SECTION 2 — TEST STRATEGY BY DOMAIN

DOMAIN	PRIMARY LAYER FOCUS	COVERAGE TARGET	OWNER
Customer journey	L4 + L8	100% P1 scenarios	_____
Regulatory / compliance	L4 + L6	100% obligations	_____
Performance / scale	L5	All NFRs evidenced	_____
Security	L5 + L6	OWASP top 10 + pen	_____
Disaster recovery	L5 + L7	RTO/RPO proven	_____
Operational	L7	Run-book validated	_____

Each domain has dedicated test lead reporting to QA Director.

INDEPENDENT ASSURANCE AND EVIDENCE

SECTION 3 — INDEPENDENT ASSURANCE LAYERS

Reviews independent of build team. Required for board-level sign-off.

REVIEW TYPE	REVIEWER	FREQUENCY	REPORTS TO
Architecture review	Independent ARB	Per release	CTO
Security audit	External pen-test	Half-yearly	CISO
Code quality audit	External auditor	Annual	CTO
Programme assurance	Independent reviewer	Quarterly	Sponsor / Board
Internal audit	Internal Audit	Risk-based	Audit Committee
Regulatory inspection	Regulator	As req	CRO / Board

Findings tracked centrally with SLA for closure; aged findings reported to Audit Committee.

SECTION 4 — EVIDENCE AND SIGN-OFF

Per release evidence pack

Test results · NFR results · scan results · ARB minutes · sign-offs · audit findings

Storage Immutable archive · 7-year retention (or per regulatory requirement)

Sign-off matrix

RELEASE TYPE	SIGNATURES REQUIRED
Minor (point release)	QA Lead, Service Owner
Major (feature release)	QA Lead, Architect, CISO, Service Owner, BO
Tranche / programme	All above + Sponsor + Independent reviewer + Board

No release without complete evidence pack

Pack auto-assembled from CI/CD, audit logs, ARB outputs · reviewed by Release Manager pre-deploy.

QUALITY LAYERS AND STRATEGY

QUALITY PYRAMID — 8 LAYERS, ALL ACTIVE



Pyramid health: ~12,800 unit tests, ~2,400 component, ~840 integration, ~1,470 E2E. Healthy ratio.

TEST STRATEGY BY DOMAIN

DOMAIN	PRIMARY LAYERS	COVERAGE TARGET	OWNER
Customer onboarding	L4 + L8	100% P1 (180 scen.)	D. Lin (Test Lead)
Lending decisioning	L4 + L6	100% rules (310 cases)	M. Park (Cred Risk)
APRA / AUSTRAC reg	L4 + L6	100% obligations	P. Walsh (Compliance)
Performance / scale	L5	5,000 TPS sustained	A. Hassan (Perf Eng)
Security (CPS 234)	L5 + L6	OWASP + APRA pen	CISO Team
Disaster recovery	L5 + L7	RTO 30m / RPO 5m	Operations
Operational readiness	L7	Run-book validated	Ops Director

7 named domain test leads. APRA CPS 234 obligations cross-cut all 7 — explicit traceability matrix maintained.

INDEPENDENT ASSURANCE AND EVIDENCE

INDEPENDENT ASSURANCE LAYERS — APRA-ALIGNED

REVIEW TYPE	REVIEWER	FREQUENCY	REPORTS TO
Architecture review	Independent ARB	Per release	CTO
Penetration test	CREST-cert vendor	Half-yearly	CISO + Audit Cmte
CPS 234 audit	Big-4 firm	Annual	CISO + Board
Code quality review	External engineering	Annual	CTO
Programme assurance	Independent reviewer	Quarterly	Sponsor / Board
Internal audit	Internal Audit	Risk-based	Audit Committee
APRA inspection	APRA	As required	CRO / Board

Findings tracked in central register · SLA: high 30d, med 90d, low 180d · aged findings to Audit Cmte monthly

EVIDENCE AND SIGN-OFF

Per release evidence pack contains:

Test results (auto from pipeline) · NFR proof · OWASP scan · pen-test summary · ARB minutes · sign-offs

Storage Immutable archive (S3 Object Lock) · 7-year retention per APRA prudential standards

Sign-off matrix

RELEASE TYPE	SIGNATURES REQUIRED
Hotfix / patch	QA Lead, Service Owner
Minor (point release)	QA Lead, Architect, Service Owner
Major (feature release)	QA Lead, Architect, CISO, Service Owner, Business Owner
Tranche / programme	All above + Sponsor + Independent reviewer + APRA notified

Release pipeline gated · evidence pack auto-assembled · Release Manager (weekly rotation) verifies completeness pre-deploy.

CHANGE IMPACT AND WORKFORCE PLAN

SECTION 1 — CHANGE IMPACT HEATMAP

Each affected role / unit rated on impact dimensions: process, system, role, location.

ROLE / GROUP	PROCESS	SYSTEM	ROLE	POPULATION	SUM
Group 1	H/M/L	H/M/L	H/M/L	_____	H/M/L
Group 2	H/M/L	H/M/L	H/M/L	_____	H/M/L
Group 3	H/M/L	H/M/L	H/M/L	_____	H/M/L
Group 4	H/M/L	H/M/L	H/M/L	_____	H/M/L
Group 5	H/M/L	H/M/L	H/M/L	_____	H/M/L

Typical Gold scope: 8–25 affected groups identified. Detailed register in supporting paper.

High-impact groups receive dedicated change leads.

SECTION 2 — WORKFORCE TRANSITION

Roles changing, created, retired. Reskilling pathway. Union / FWC engagement.

CATEGORY	FTE	PATHWAY	OWNER
Roles retired	_____	Reskill / redeploy / severance	CHRO
Roles changed	_____	In-role training, certification	CHRO + line
Roles created	_____	Internal mobility + external hire	CHRO
Locations affected	_____	Site-specific transition plan	Property + HR

Union / FWC engagement Consultation periods met · agreements documented · grievance process active

FWC = Fair Work Commission. Consultation periods are legal obligations, not options.

LIFECYCLE, ADOPTION, RESISTANCE

SECTION 3 — CHANGE LIFECYCLE

Five-phase model with deliverables and exit criteria per phase.



Per phase exit criteria:

Prepare → Sponsor coalition signed; impact heatmap complete
Plan → Training, comms, network plans approved by Sponsor
Deliver → Champions trained; first wave delivered with feedback closed
Embed → Adoption ≥ 80% target; resistance hot-spots remediated
Sustain → Programme team disbanded; BAU owns change network
Phase exit gates reviewed at Programme Board.

SECTION 4 — ADOPTION AND RESISTANCE MANAGEMENT

Adoption metrics (tracked weekly, reported monthly)

Active users · feature usage · self-service rate · ticket volume by category
Confidence pulse (4-question survey) · NPS for the change · stay-rate

Resistance hot-spot protocol

Identified by adoption metrics or pulse survey · escalated to Change Lead within 48 hours
Diagnostic conversation with affected group · root cause categorised · intervention designed
Outcome reported back to group · closed-loop tracking until adoption returns to target

Champions network

~1 champion per 25 affected staff · trained, recognised, given dedicated time (2hr / week)

Sponsor cadence

Visible Sponsor presence at all-hands; resistance hot-spots escalated to Sponsor for direct engagement

CHANGE IMPACT AND WORKFORCE PLAN

CHANGE IMPACT HEATMAP — 11 GROUPS, ~14,200 STAFF

ROLE / GROUP	PROCESS	SYSTEM	ROLE	POPULATION	SUM
Doctors (consultants + reg.)	H	H	M	~3,200	H
Nurses (RN + EN)	H	H	H	~6,200	H
Allied health	M	H	M	~1,400	M
Admin / clerical	H	H	H	~1,800	H
Pharmacy	M	H	L	~280	M
Pathology / Imaging	L	M	L	~620	L
ED / Critical Care	H	H	M	~720	H

5 of 11 groups rated High overall: Doctors, Nurses, Admin, Pharmacy (system H), ED — each gets a dedicated change lead.

Critical risk: Nurses (~6,200) is the largest high-impact group; failure here = patient safety event.

WORKFORCE TRANSITION

CATEGORY	FTE	PATHWAY	OWNER
Health Information clerks	~140 retired	Reskill to digital health roles · 18-month pathway	CHRO
Bedside nurses (workflow)	~6,200 changed	Refresh + EMR competency · 12-week module	CNIO
Junior doctors (charting)	~1,200 changed	Embedded training in clinical rotations	CMIO
Clinical informatics	~85 created	Internal mobility from nursing/pharmacy + 14 external	CHRO + CMIO
Locations affected	8 hospitals	Site-specific transition plans (per CMIO and DON)	DONs

ANMF / AMA / HSU engagement Quarterly consultations active since Mar 2026 · MOU on training entitlement signed

ANMF = Aust Nursing & Midwifery Federation. Consultation period 60 days minimum per state award. Severance not currently anticipated for any group.

LIFECYCLE, ADOPTION, RESISTANCE

CHANGE LIFECYCLE — CURRENT POSITION

PREPARE	PLAN	DELIVER	EMBED	SUSTAIN
11 groups mapped Coalition signed Q1	Comms + training approved Mar'26	CURRENT Pilot site live	Q3 FY27	FY29 onwards

Phase exit gates — current status:

- ✓ **Prepare** · Sponsor coalition (CEO, CMO, CNO, CMIO, CNIO) signed, 14 March 2026
- ✓ **Plan** · Training, comms, network plans approved by ExCo, 8 May 2026
- ⚡ **Deliver** · 142 champions trained · pilot site (Royal Hospital) live 19 Sep 2026
- ○ **Embed** · Adoption ≥ 80% target · gate review Q3 FY27 (post-rollout +90 days)
- ○ **Sustain** · Programme team disband · BAU owns network · FY29

Phase reviewed at Programme Board · Clinical Reference Group has formal veto on workflow changes mid-phase.

ADOPTION AND RESISTANCE — PILOT SITE METRICS

Adoption (week 6 post-go-live)

Active users 94% (target 90%) · core flow daily usage 81% (target 75%)
Self-service rate 67% (target 70% by W12) · ticket volume below forecast
Confidence pulse 3.8/5 (target ≥ 4.0 by W12) — improving weekly

Resistance hot-spots active

HS-1 ED nurses (after-hours): workflow gaps in trauma pathway · CNIO + ED Director engaged 8 Oct

HS-2 Geriatric ward consultants: documentation slowness · 1:1 coaching scheduled · CMIO sponsor

Champions network

142 champions trained (1 per ~100 staff at pilot · plan ramps to 1 per ~50 at full rollout)

Sponsor visibility

CEO at all-hands monthly · CMO walkround pilot site weekly · CNO direct line for nurse escalations

Hot-spot protocol triggered automatically by adoption metric below target · escalation to Change Director within 48h.

SERVICE MODEL AND SLAs

SECTION 1 — SERVICE DEFINITION

Each service in scope: ownership, dependencies, business criticality.

SERVICE	OWNER	CRITICALITY	RTO / RPO	SUPPORT
Service 1	_____	Tier ___	__/__min	24×7
Service 2	_____	Tier ___	__/__min	24×7
Service 3	_____	Tier ___	__/__min	Business hrs
Service 4	_____	Tier ___	__/__min	Business hrs
Service 5	_____	Tier ___	__/__min	Business hrs

Tier 1 = mission-critical · Tier 2 = important · Tier 3 = supporting. Drives RTO/RPO commitments.

SECTION 2 — SLAs / SLOs

Service-level objectives, error budgets, escalation thresholds.

METRIC	TARGET	ERROR BUDGET	ESCALATION
Availability	__.__%	__ min/month	>50% spent → freeze
Latency p99	__ ms	__% breach OK	Sustained breach → page
Error rate	__%	__% sustained	Spike → on-call
MTTR (incident)	__ min	P1 cap	Beyond → exec brief
Change failure rate	<__%	Per quarter	Trend → review CAB

Error budget exhaustion = release freeze

Forces ops focus over feature delivery; reset monthly. Standard SRE pattern.

RUN-BOOK AND INCIDENT RESPONSE

SECTION 3 — RUN-BOOK CONTENTS

Procedures Operations executes. Maintained alongside the system.

Daily operations

Health checks · log review · backup verification · capacity check

Routine procedures

User provisioning · access changes · scheduled jobs · reporting cycles

Change procedures

Standard changes · normal changes · emergency changes · rollback

Incident response

By incident class · escalation tree · communication scripts · post-mortem template

Disaster recovery

Failover procedure · data restoration · service prioritisation

SECTION 4 — INCIDENT MANAGEMENT

CLASS	DESCRIPTION	RESPONSE	REPORT TO
SEV-1	Service down, data loss, security	Page · Bridge open	CEO + Board
SEV-2	Major degradation, T1 impact	Page on-call · 30m	CIO + Sponsor
SEV-3	Limited impact, workaround	Standard ticket	Service Owner
SEV-4	Cosmetic / informational	Backlog	Service Owner

Post-mortem

All SEV-1 / SEV-2 within 5 business days · blameless · published to engineering org

External notification

Customers / regulator notified within window per SLA / regulatory obligation

Lessons-learned register tracked monthly; recurring patterns drive retros and process change.

SERVICE MODEL AND SLAs

SERVICE DEFINITION — 7 SERVICES, 22 SITES

SERVICE	OWNER	CRIT.	RTO/RPO	SUPPORT
WMS Core	D. Park (Ops Director)	T1	15 / 5 min	24×7
RF gun fleet (2,400)	M. Allen (Tech Ops)	T1	30 / 1 min	24×7
TMS Integration	P. Kumar (Integration Lead)	T1	15 / 5 min	24×7
ERP Stock Reconciliation	L. Tran (Finance Systems)	T2	2h / 1h	Bus. hrs
Returns & Disposal	S. Wood (Returns Mgr)	T2	4h / 1h	Bus. hrs
Reporting & Analytics	A. Suresh (BI Lead)	T3	1d / 1d	Bus. hrs
Self-service portal	J. Reeves (Customer Ops)	T3	8h / 4h	Bus. hrs

Service catalogue published in Confluence · BAU service owners signed Sept 2026 · DR test schedule: T1 every 6mo, T2 every 12mo

SLAs / SLOs — TIER 1 SERVICES (WMS CORE, RF GUNS, TMS)

METRIC	TARGET	ERROR BUDGET	ESCALATION
Availability	99.95%	22 min/month	>50% spent → freeze
Latency p99 (pick scan → response)	~~wait~~ —	— shifted —	— see below —
Latency p99 RF transactions	≤ 220 ms	2% breach OK	Sustained → page on-call
Error rate (5xx)	< 0.1%	0.5% sustained 15m	Spike → on-call
MTTR (P1 incidents)	≤ 30 min	3 P1 / quarter cap	>30m → exec brief
Change failure rate	< 5%	Per quarter	Trend → CAB review

Error budget exhaustion → release freeze + retro

SRE practice · forces ops focus over feature shipping when reliability erodes · resets monthly with executive review.

RUN-BOOK AND INCIDENT RESPONSE

RUN-BOOK CONTENTS — 87 PROCEDURES, ALL VALIDATED

Daily operations (12 procedures)
Health checks · log review · backup verification · capacity check · peak-day prep

Routine procedures (24 procedures)
User provisioning · access changes · scheduled jobs · reporting cycles · stocktake

Change procedures (18 procedures)
Standard, normal, emergency · CAB process · rollback runbook · canary deploy

Incident response (22 procedures)
By incident class · escalation tree · scripts · post-mortem template (blameless)

Disaster recovery (11 procedures)
Failover (validated 14 Jul 2026, RTO 12m actual) · data restore · service prioritisation

All 87 procedures pressure-tested in DR drill 14 Jul 2026 · 9 procedures revised post-drill · re-test passed 28 Jul.

INCIDENT MANAGEMENT — POST-LAUNCH 90 DAYS

CLASS	DESCRIPTION	Q3 COUNT	MEDIAN MTTR
SEV-1	Service down, T1 blocked	2 (cap 3)	22 min ✓
SEV-2	Major degradation	8	1h 14 min
SEV-3	Limited impact, workaround	37	4h 38 min
SEV-4	Cosmetic / informational	82	backlog

Post-mortem outcomes
10/10 SEV-1/2 published in 5 days · 4 systemic patterns identified · 2 architecture changes booked

Customer notification
SEV-1 status page within 5 min · email customers within 30 min · regulator within obligation window

Patterns retro held monthly · service architecture team owns systemic remediation · Audit Committee briefed on aged SEV-1/2.

BENEFITS REALISATION

SECTION 1 — BENEFITS REGISTER (FROM STRATEGIC BUSINESS CASE)

BENEFIT	CATEGORY	BASELINE	TARGET	OWNER	REVIEW
B-01	_____	_____	_____	_____	_____
B-02	_____	_____	_____	_____	_____
B-03	_____	_____	_____	_____	_____
B-04	_____	_____	_____	_____	_____
B-05	_____	_____	_____	_____	_____

Each benefit reconciles back to a Strategic Business Case line item · Owner is named director or higher · No "phantom benefits".


Categories used at Gold scale:

Cost savings · Revenue uplift · Risk reduction · Capacity created · Compliance assurance · Customer experience · Workforce capability

Each category has its own measurement methodology to avoid double-counting across benefits.

SECTION 2 — REALISATION PROFILE AND CASH RECONCILIATION

Annual benefit profile · year-on-year reconciliation to actual financials.

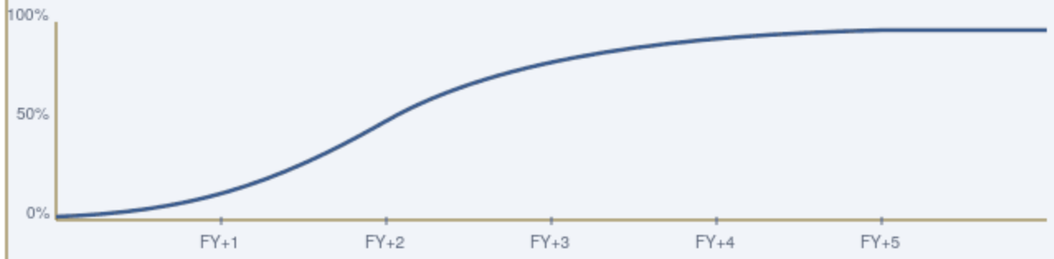

Reconciliation: Annual benefits compared to financial actuals (CFO Office certifies)

Variance > 15% triggers re-baselining of remaining profile · sponsor accountable for assumption integrity.

PROGRAMME RISK MANAGEMENT

SECTION 3 — RISK HEATMAP (RESIDUAL, POST-MITIGATION)

Likelihood × Impact · each risk owned at executive level.

	LOW	MEDIUM	HIGH	EXTREME
EXTREME				
HIGH		5	3	
MED	2			2
LOW				

Number of risks per cell

Top-right risks reported to Board monthly.

Risks plotted post-mitigation. Pre-mitigation view in supporting risk register.

SECTION 4 — TOP RISKS WITH OWNERS

R1. _____

Owner: _____ · Likelihood: ____ · Impact: ____ · Mitigation: _____

R2. _____

Owner: _____ · Likelihood: ____ · Impact: ____ · Mitigation: _____

R3. _____

Owner: _____ · Likelihood: ____ · Impact: ____ · Mitigation: _____

R4. _____

Owner: _____ · Likelihood: ____ · Impact: ____ · Mitigation: _____

Closure discipline

Risk closes only with executive owner sign-off; "accepted" risks documented in register

Independent challenge

Internal Audit reviews top 10 risks quarterly; reports to Audit Committee

BENEFITS REALISATION

BENEFITS REGISTER — RECONCILED TO STRATEGIC BC ($420M NPV)

BENEFIT	CATEGORY	BASELINE	FY+5 TARGET	OWNER	REVIEW
B-01 Demand-response capacity	Capacity	35 MW	380 MW	COO	Q · 60mo
B-02 AER non-compliance avoided	Risk	$420M exp.	$0 (compliant)	CRO	Q · 60mo
B-03 Maintenance cost reduction	Cost	$220M/yr	$162M/yr	CFO + Ops	M · 60mo
B-04 Network efficiency revenue	Revenue	$0	$95M/yr	Retail Director	M · 60mo
B-05 Outage minutes per customer	CX	142 SAIDI	95 SAIDI	COO	M · 60mo
B-06 DER orchestration revenue	Revenue	$0	$48M/yr	Retail Director	Q · 60mo


All 6 reconcile to Strategic Business Case · CFO Office signs annual reconciliation. Cat: Capacity / Risk / Cost / Revenue / CX

No phantom benefits: Each benefit measurable in production data; no hand-waving allowed.

SAIDI = System Average Interruption Duration Index (industry standard outage metric, AER reportable).

REALISATION PROFILE — ACTUAL vs PLAN

Cumulative benefit realisation against original profile · CFO-certified annually

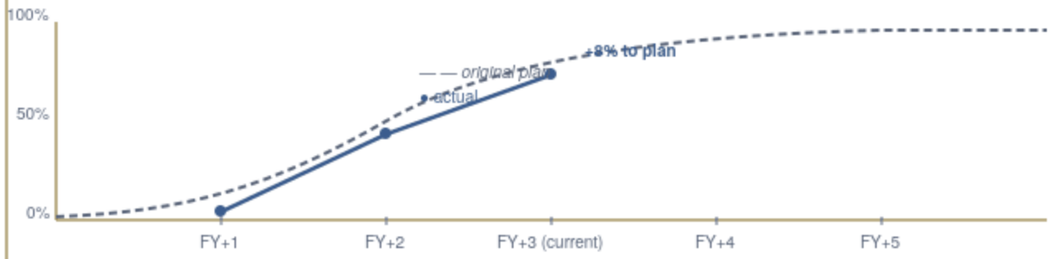

Reconciliation FY+3: Cumulative $148M realised vs $137M planned (+8%) — CFO Office certified Q3 FY29

PROGRAMME RISK MANAGEMENT

RISK HEATMAP — RESIDUAL (POST-MITIGATION) · 23 RISKS TOTAL

	LOW	MEDIUM	HIGH	EXTREME
EXTREME			1	
HIGH		5	2	2
MED	3	3	2	1
LOW	4			

Reds:
Top-right risks (red zone) reported to Board monthly

3 risks current red: cyber, customer adoption, workforce capability

Plotted post-mitigation. Pre-mitigation view in supporting risk register · 23 risks under formal management.

TOP 4 RISKS — EXECUTIVE-OWNED, BOARD-VISIBLE

R1. Cyber attack on grid telemetry — High likelihood, extreme impact
Owner: CISO · Mitigation: defence-in-depth, ASD-aligned, $48M budget · IRAP assessed half-yearly

R2. Customer DER adoption below 60% — Med likelihood, high impact
Owner: Retail Director · Mitigation: tariff incentives + Y2 pilot · cap T3 spend if < 50% by then

R3. Workforce capability gap (DER orchestration) — High, high
Owner: CHRO · Mitigation: 18mo reskilling pathway · 87 contractors backfill · TAFE partnership

R4. AER pathway changes mid-flight — Med, high · Owner: CRO
Mitigation: quarterly AER engagement · contracts permit pivot at gates · scenarios modelled

Closure discipline: Risk closes only with executive owner sign-off · 4 risks closed FY+3 (independent review)

Independent challenge: Internal Audit reviews top 10 quarterly · Audit Committee receives report · 2 findings open

All risks reconcile to Strategic Business Case risk profile · risk-adjusted NPV remains positive at $340M.
